

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: Kabir Raju G SRN: PES1UG24CS210 Jira project: Courier-Dispatch

Figure 1. Product backlog with epics, user stories, priorities and story points (Sprint 1 planned)

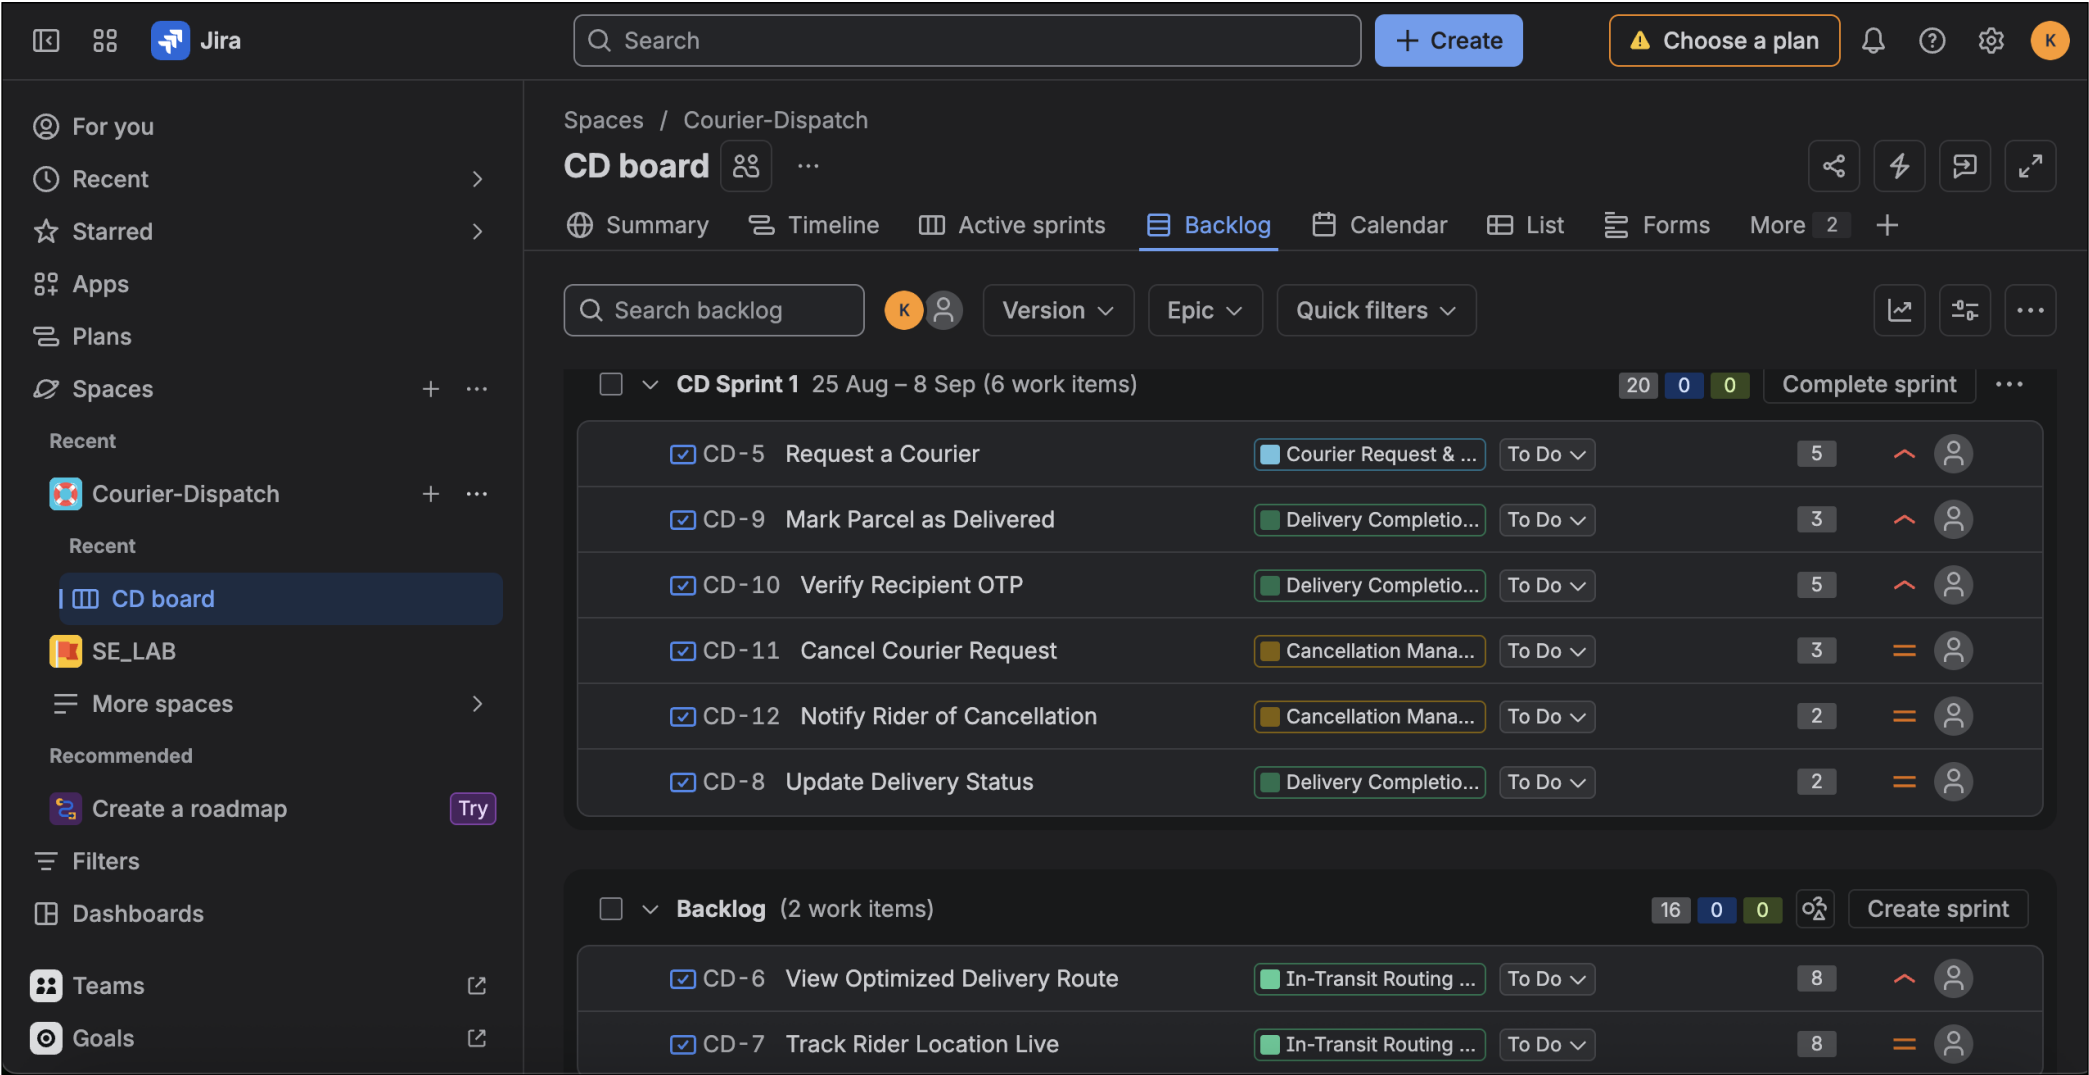


Figure 2. Epic panel showing the total story points

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Courier-Dispatch

Recent

CD board

SE_LAB

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Teams

Goals

Spaces / Courier-Dispatch

CD board

SummaryTimelineActive sprintsBacklogCalendarListFormsMore 2

Search backlog

Version

Epic

Quick filters

Epic

No epic

Courier Request & Dispatch

KeyCD-1

Work items1

Completed0

Estimate5 points

0% of estimated work complete

0 work items unestimated

View details

Create epic

CD Sprint 1 25 Aug – 8 Sep (6 work items)

2000

Complete sprint

CD-5 Request a CourierTo Do5

CD-9 Mark Parcel as DeliveredTo Do3

CD-10 Verify Recipient OTPTo Do5

CD-11 Cancel Courier RequestTo Do3

CD-12 Notify Rider of CancellationTo Do2

CD-8 Update Delivery StatusTo Do2

Backlog (2 work items)

1600

Create sprint

CD-6 View Optimized Delivery RouteTo Do8

Figure 3. Sprint 1 board, all stories in To Do

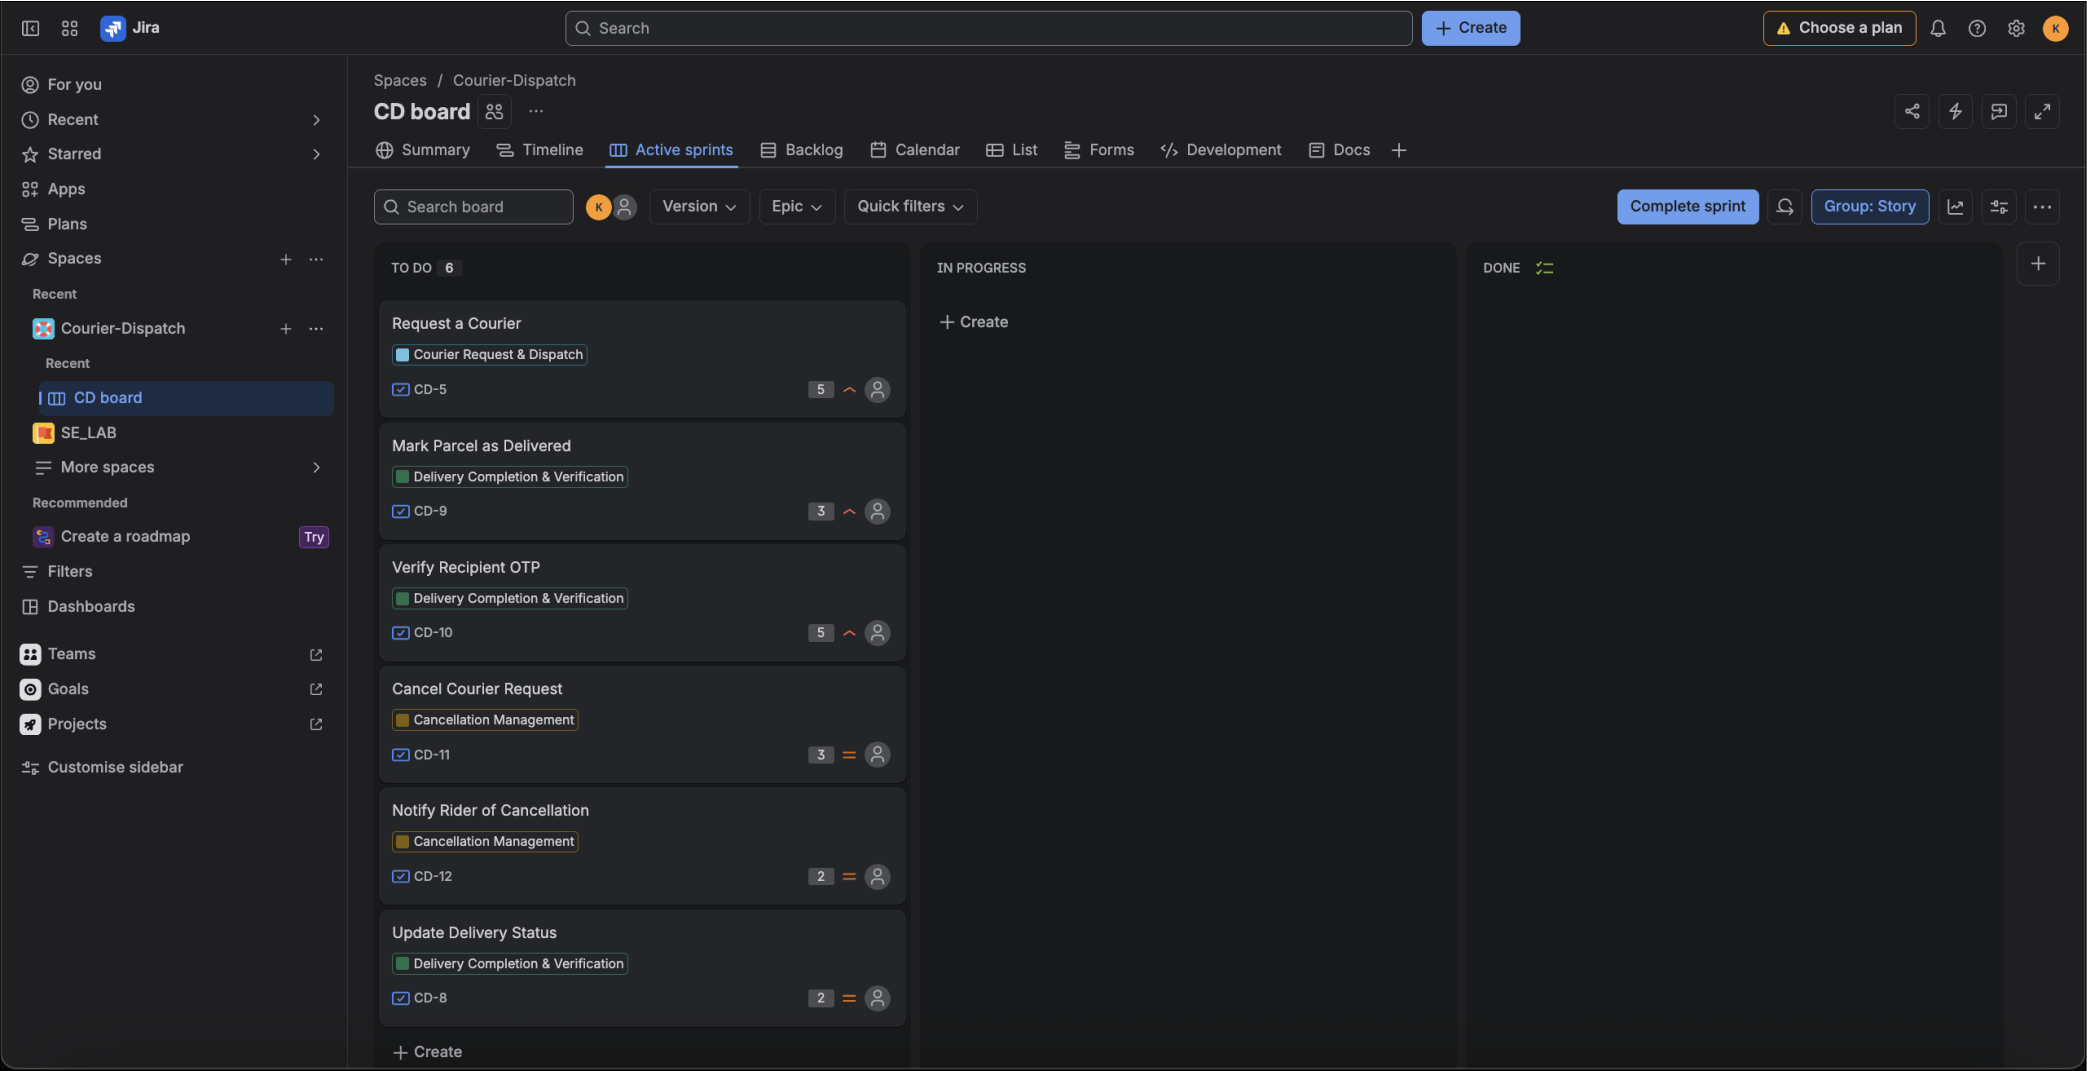


Figure 4. Sprint 1 board, first story in In Progress

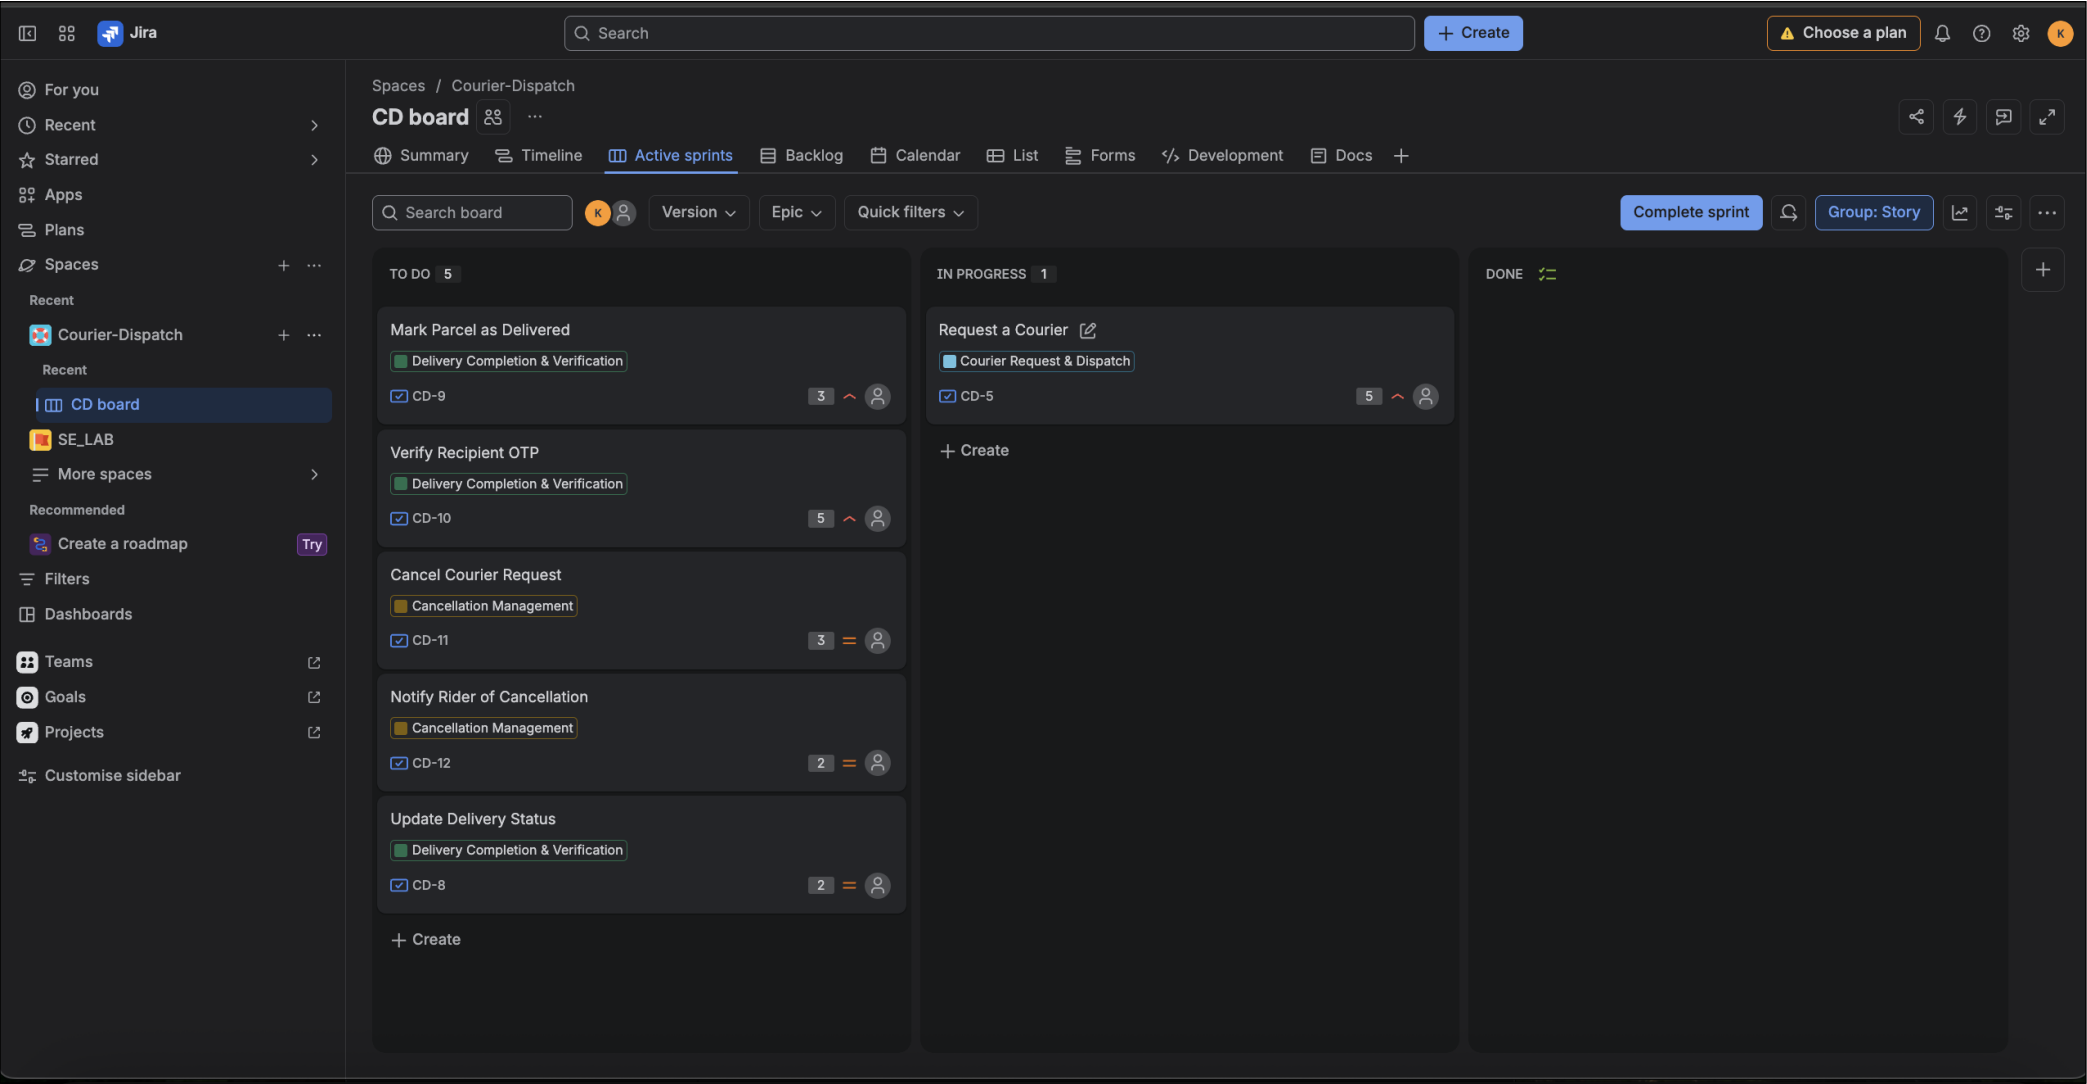


Figure 5. Sprint 1 board, first story moved to Done

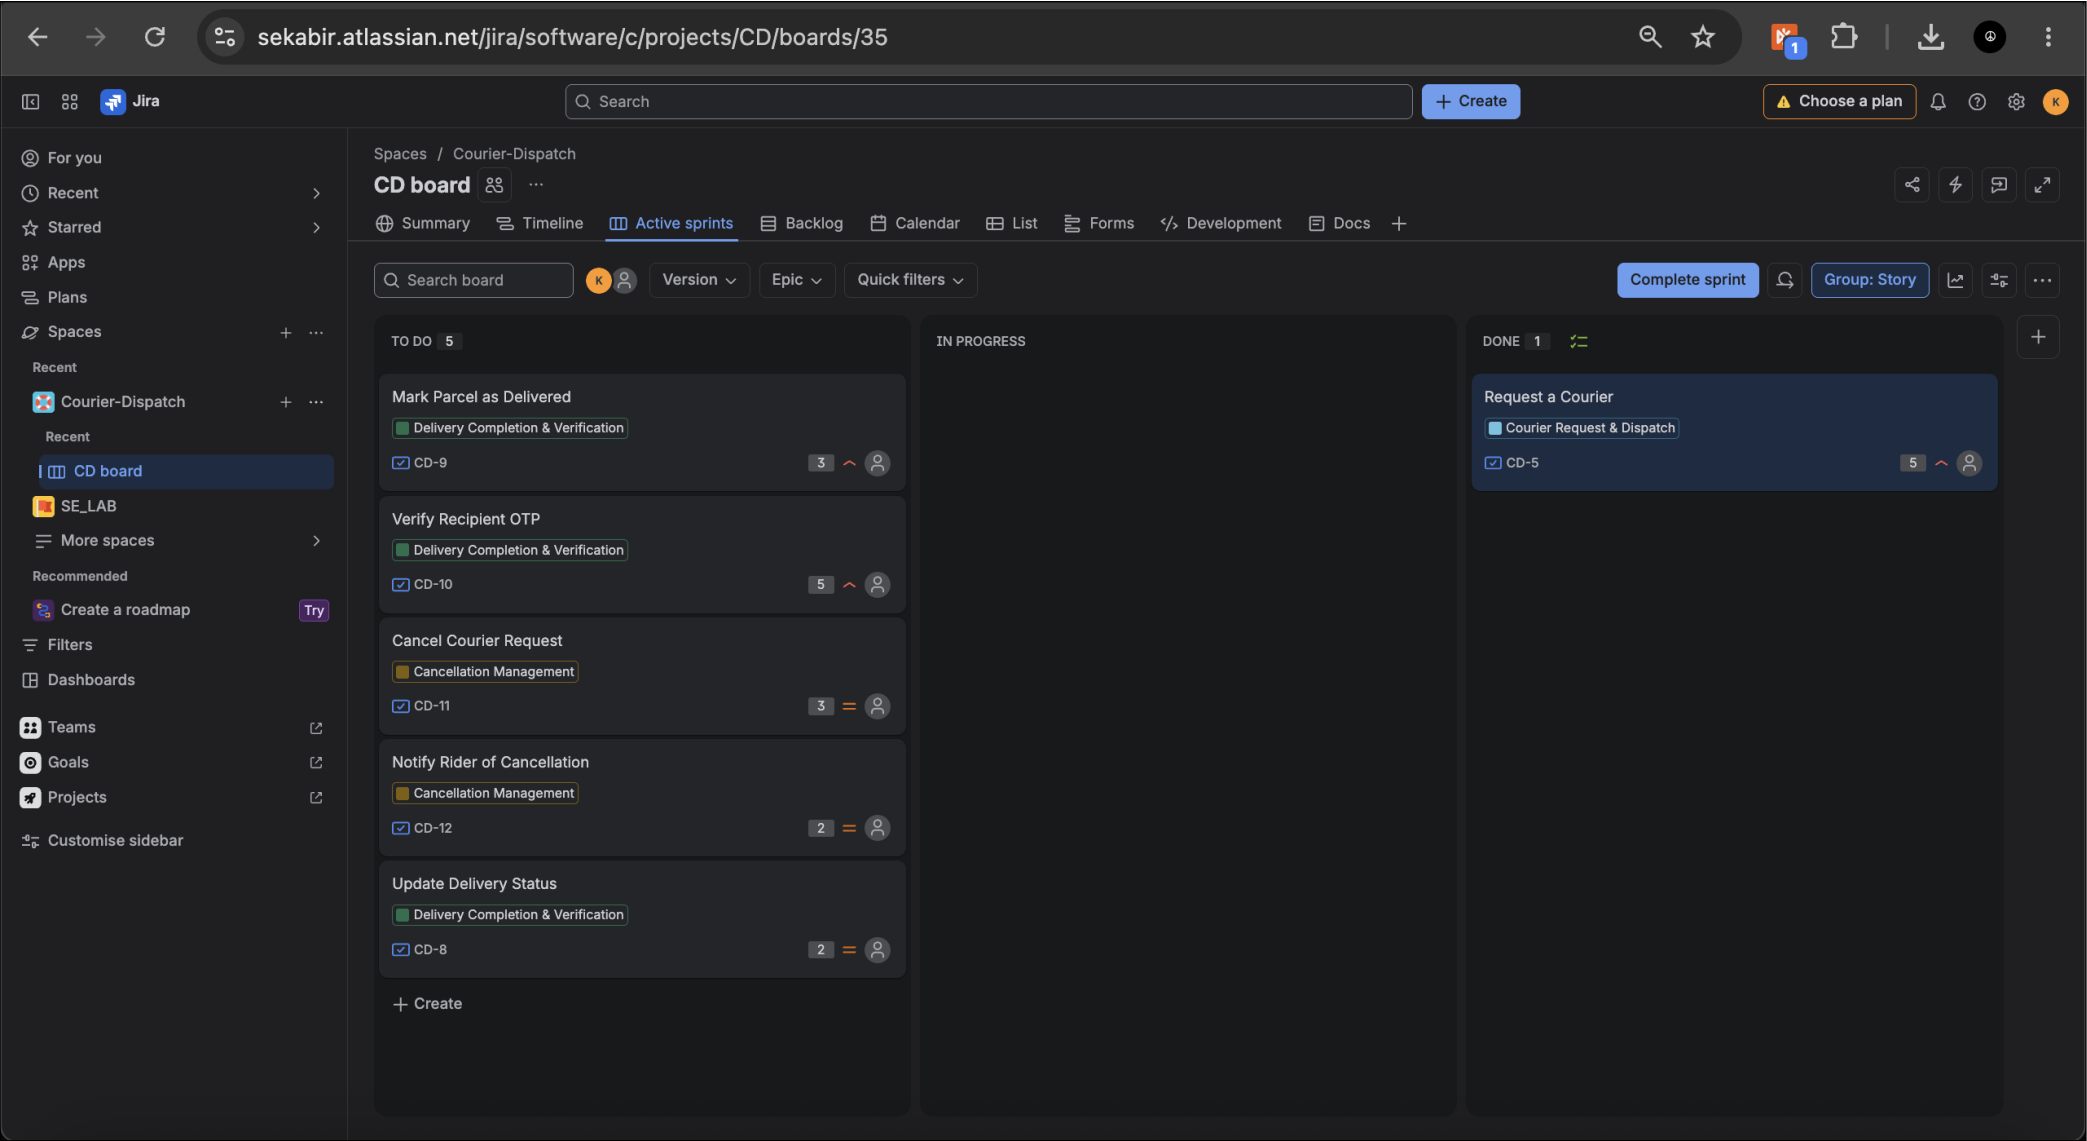


Figure 6. Sprint 1 board with stories in all three columns

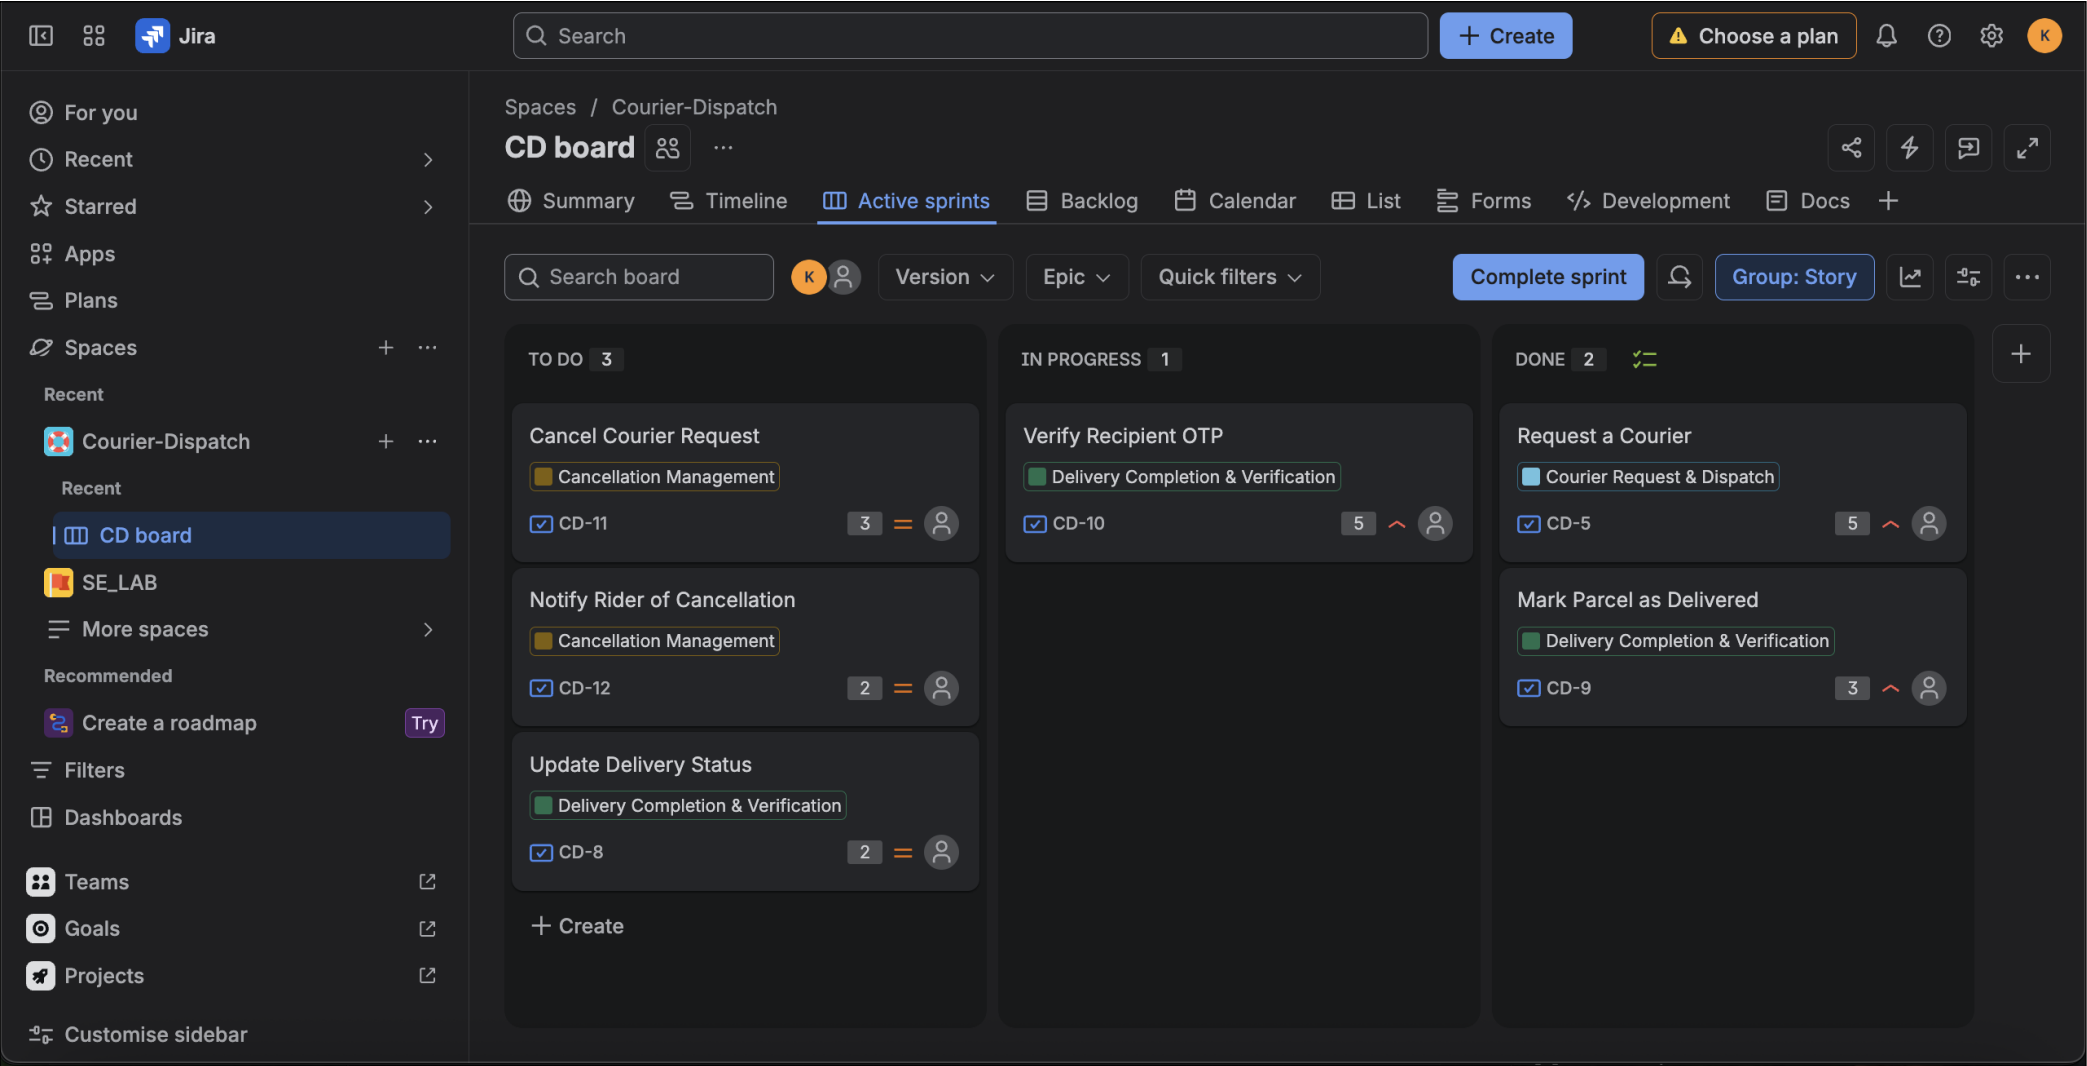


Figure 7. Sprint 1 board, all 6 stories in Done

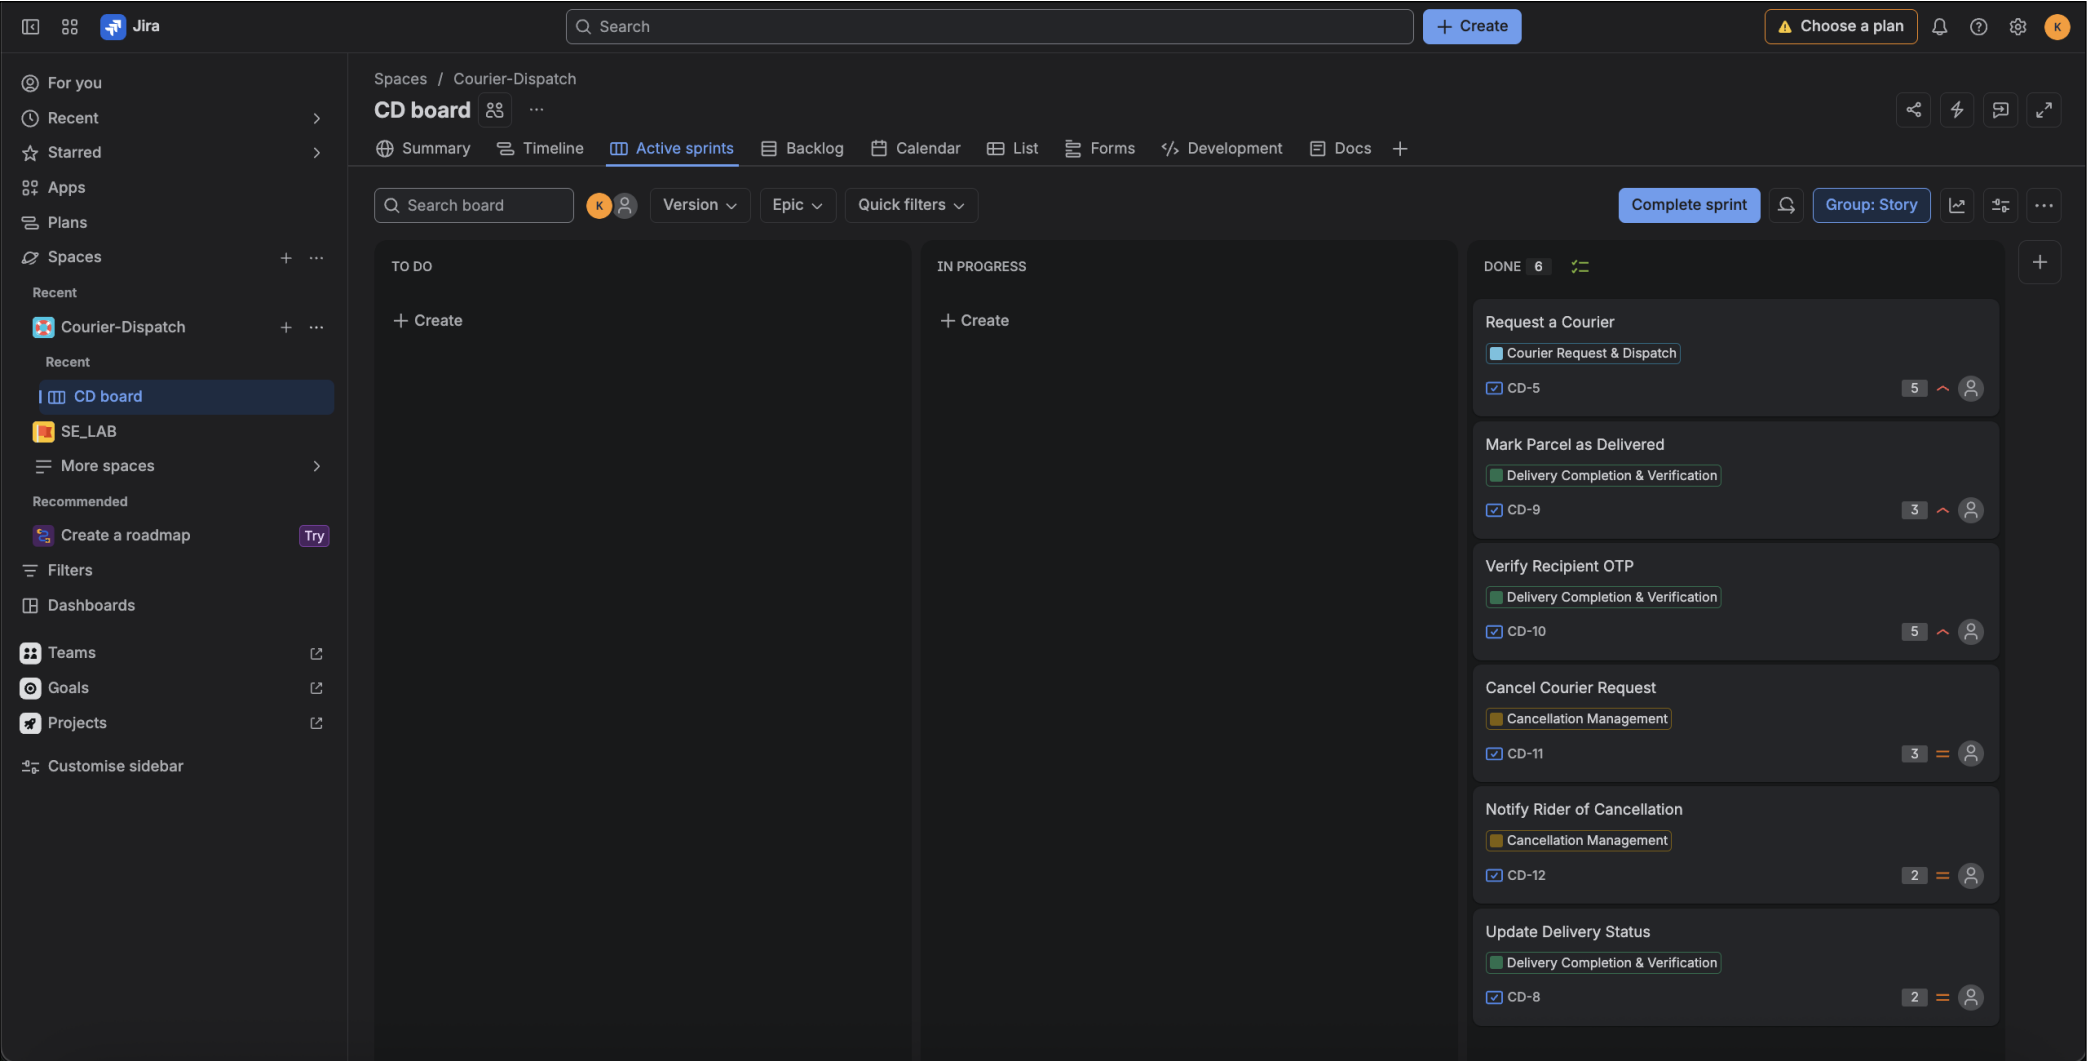


Figure 8. Complete sprint window for CD Sprint 1

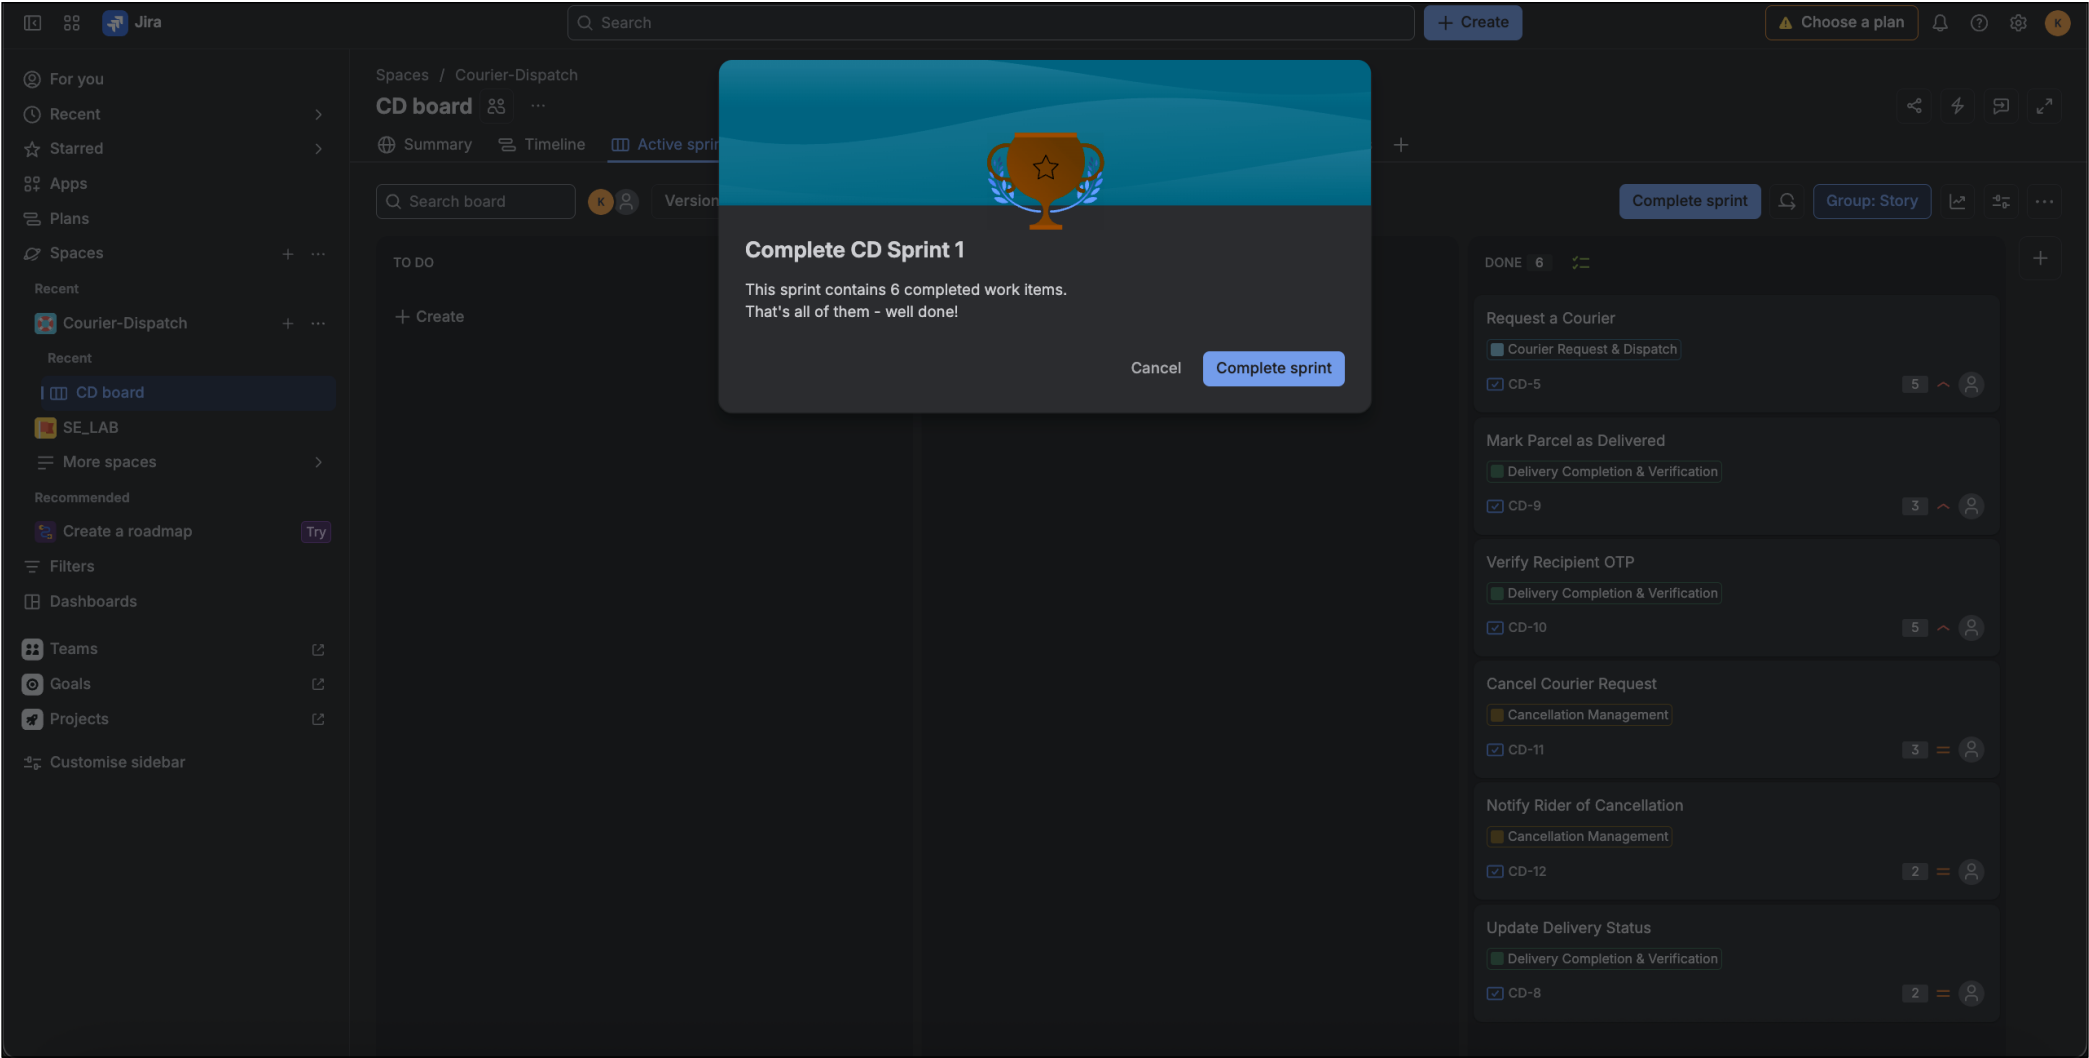


Figure 9. Backlog after Sprint 1 was completed, CD Sprint 2 created

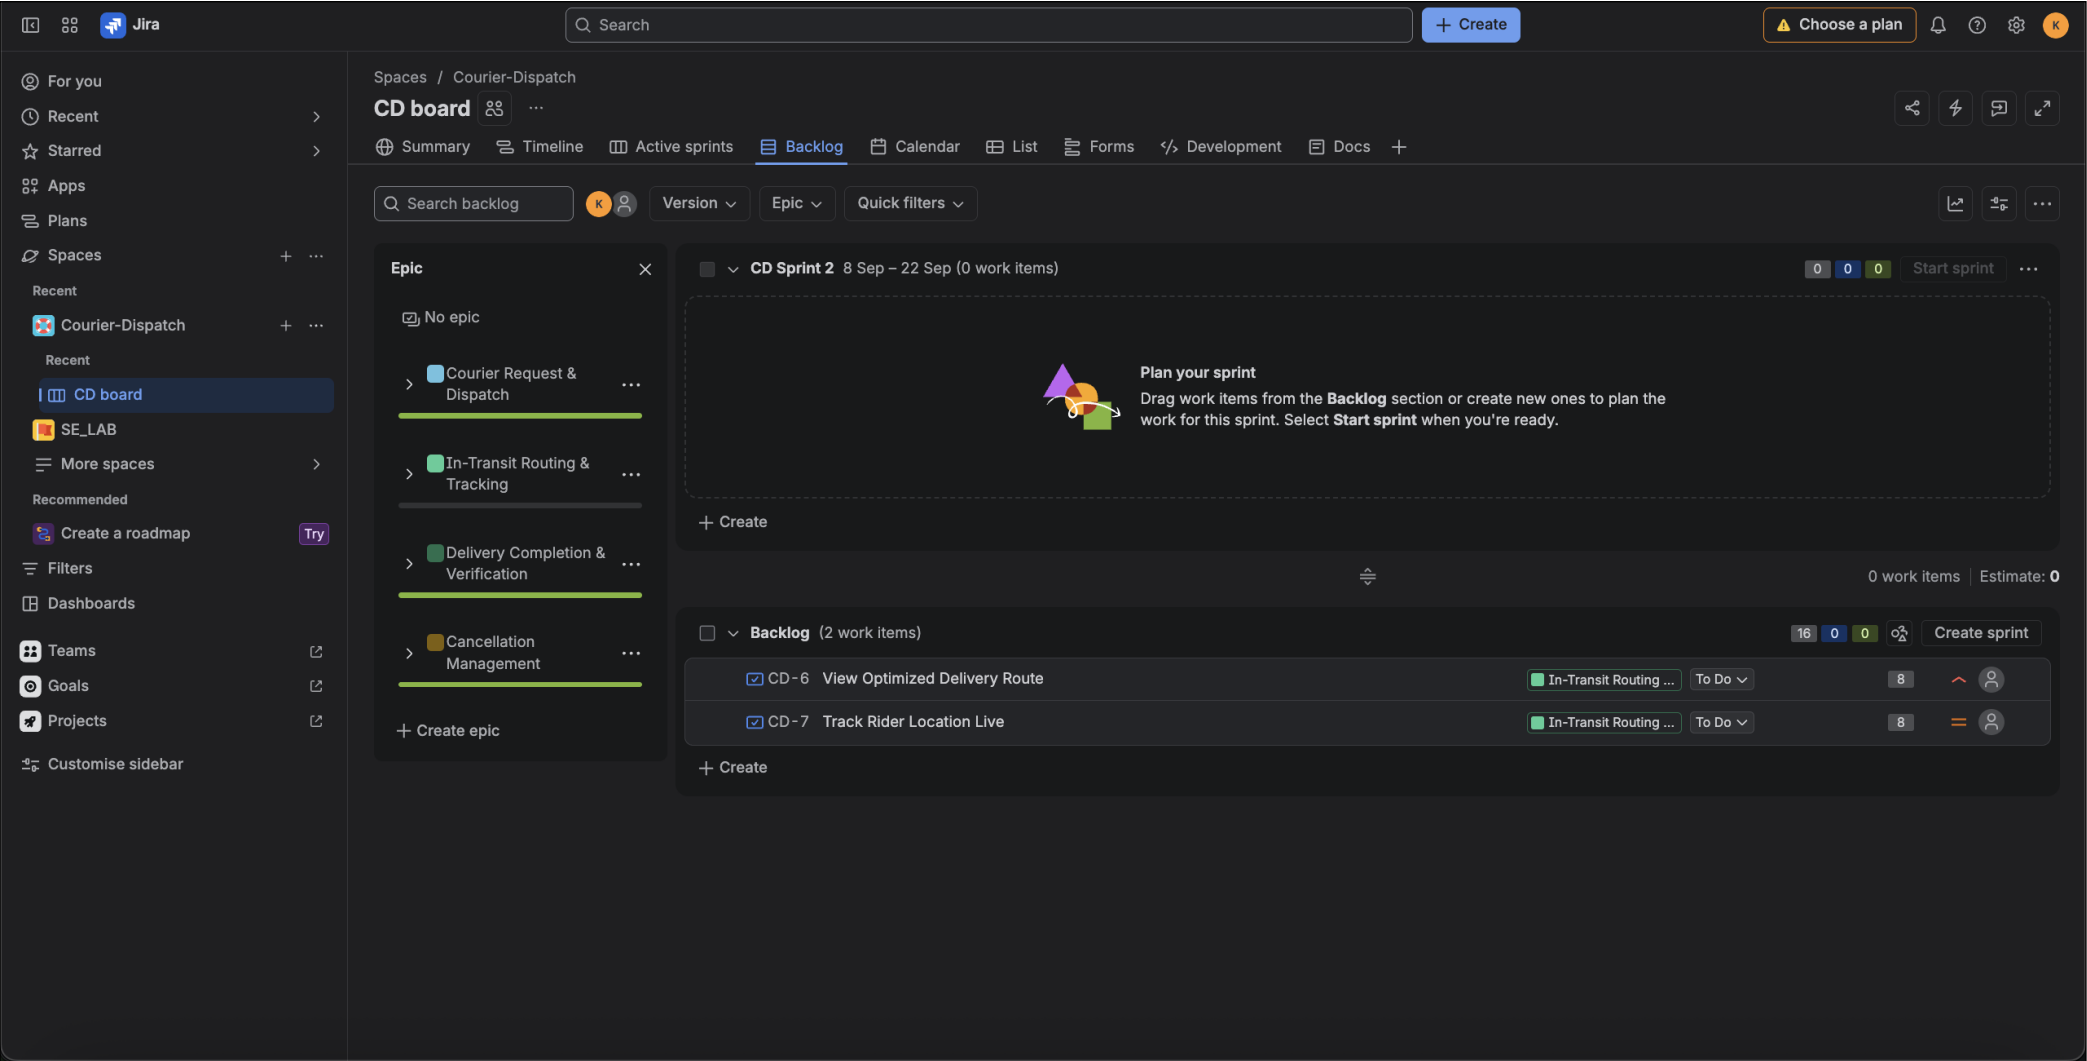


Figure 10. Burndown chart for CD Sprint 1

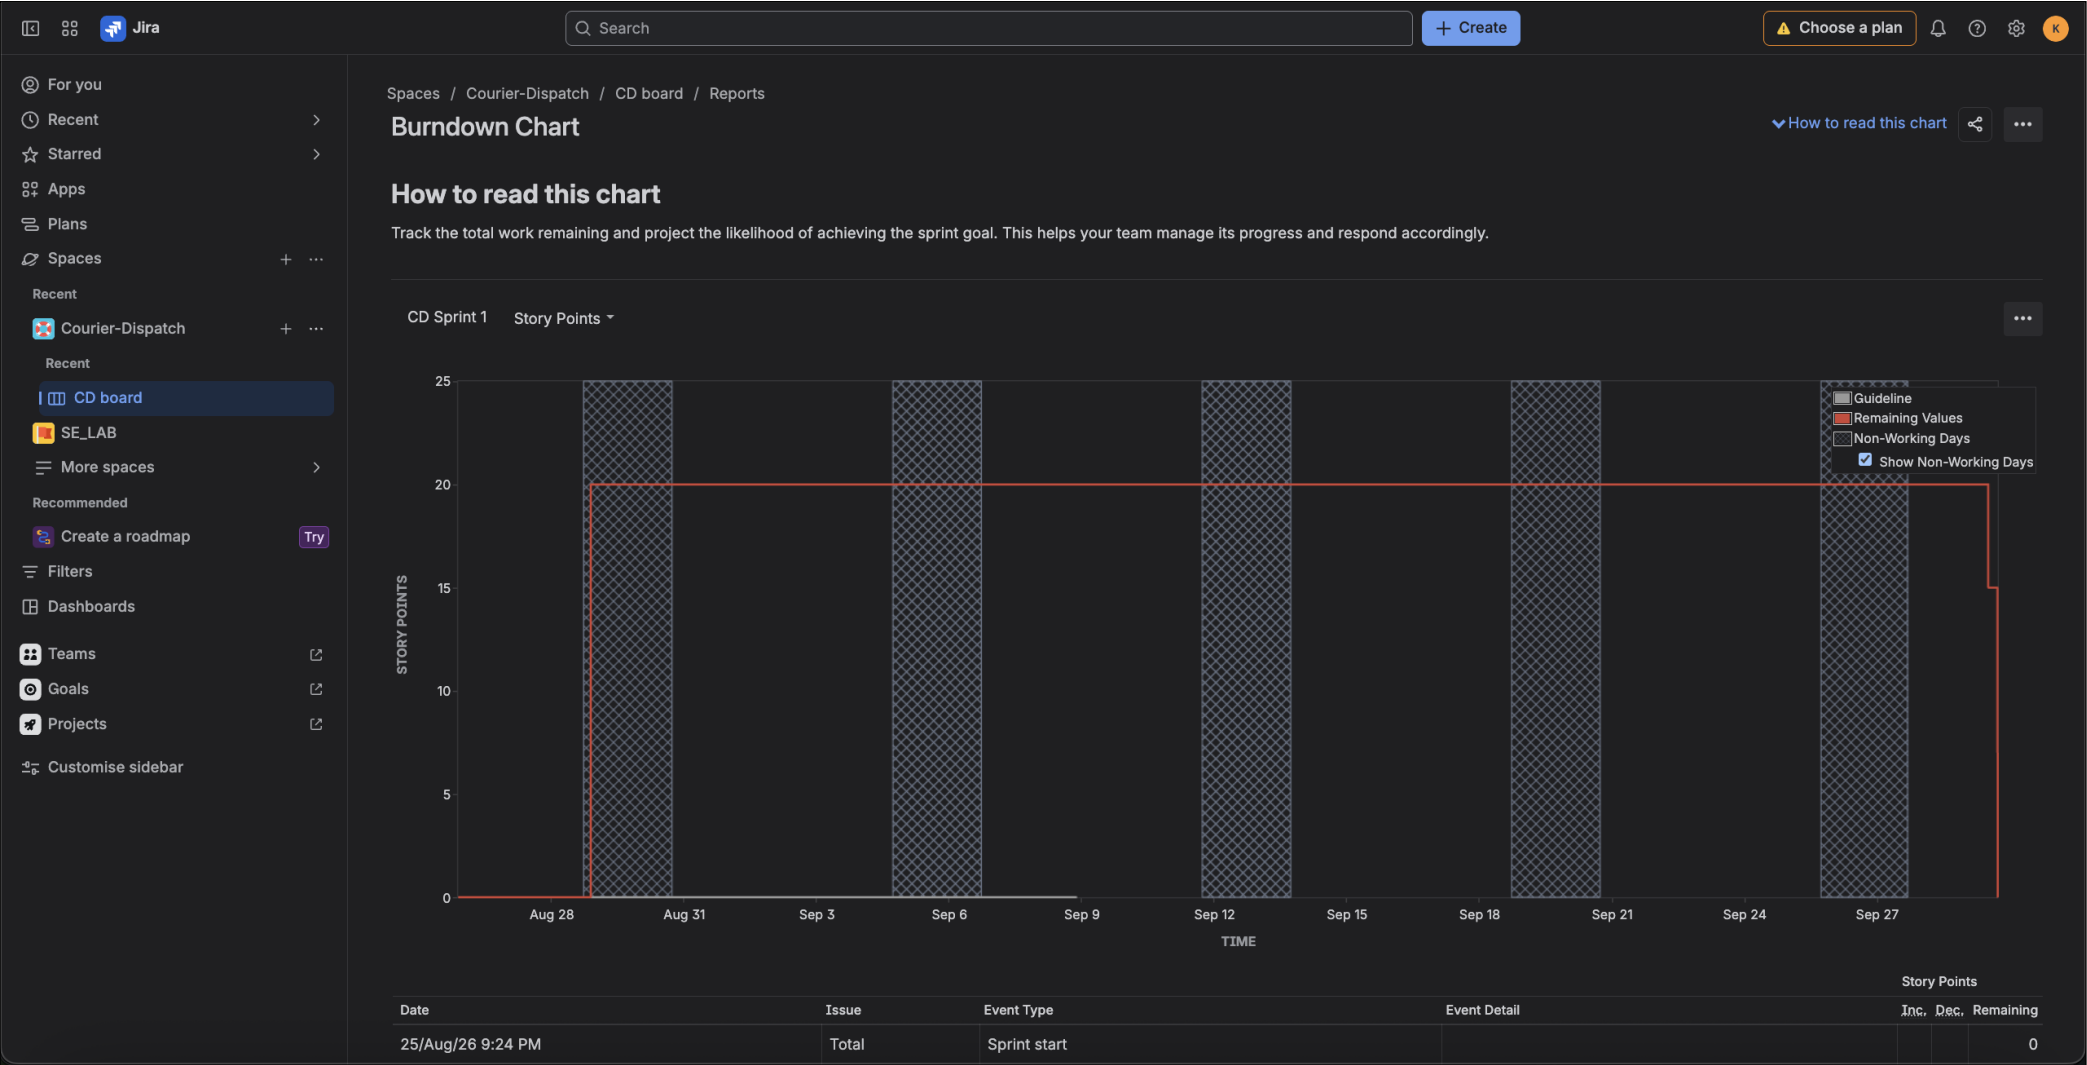


Figure 11. Burndown chart table for CD Sprint 1

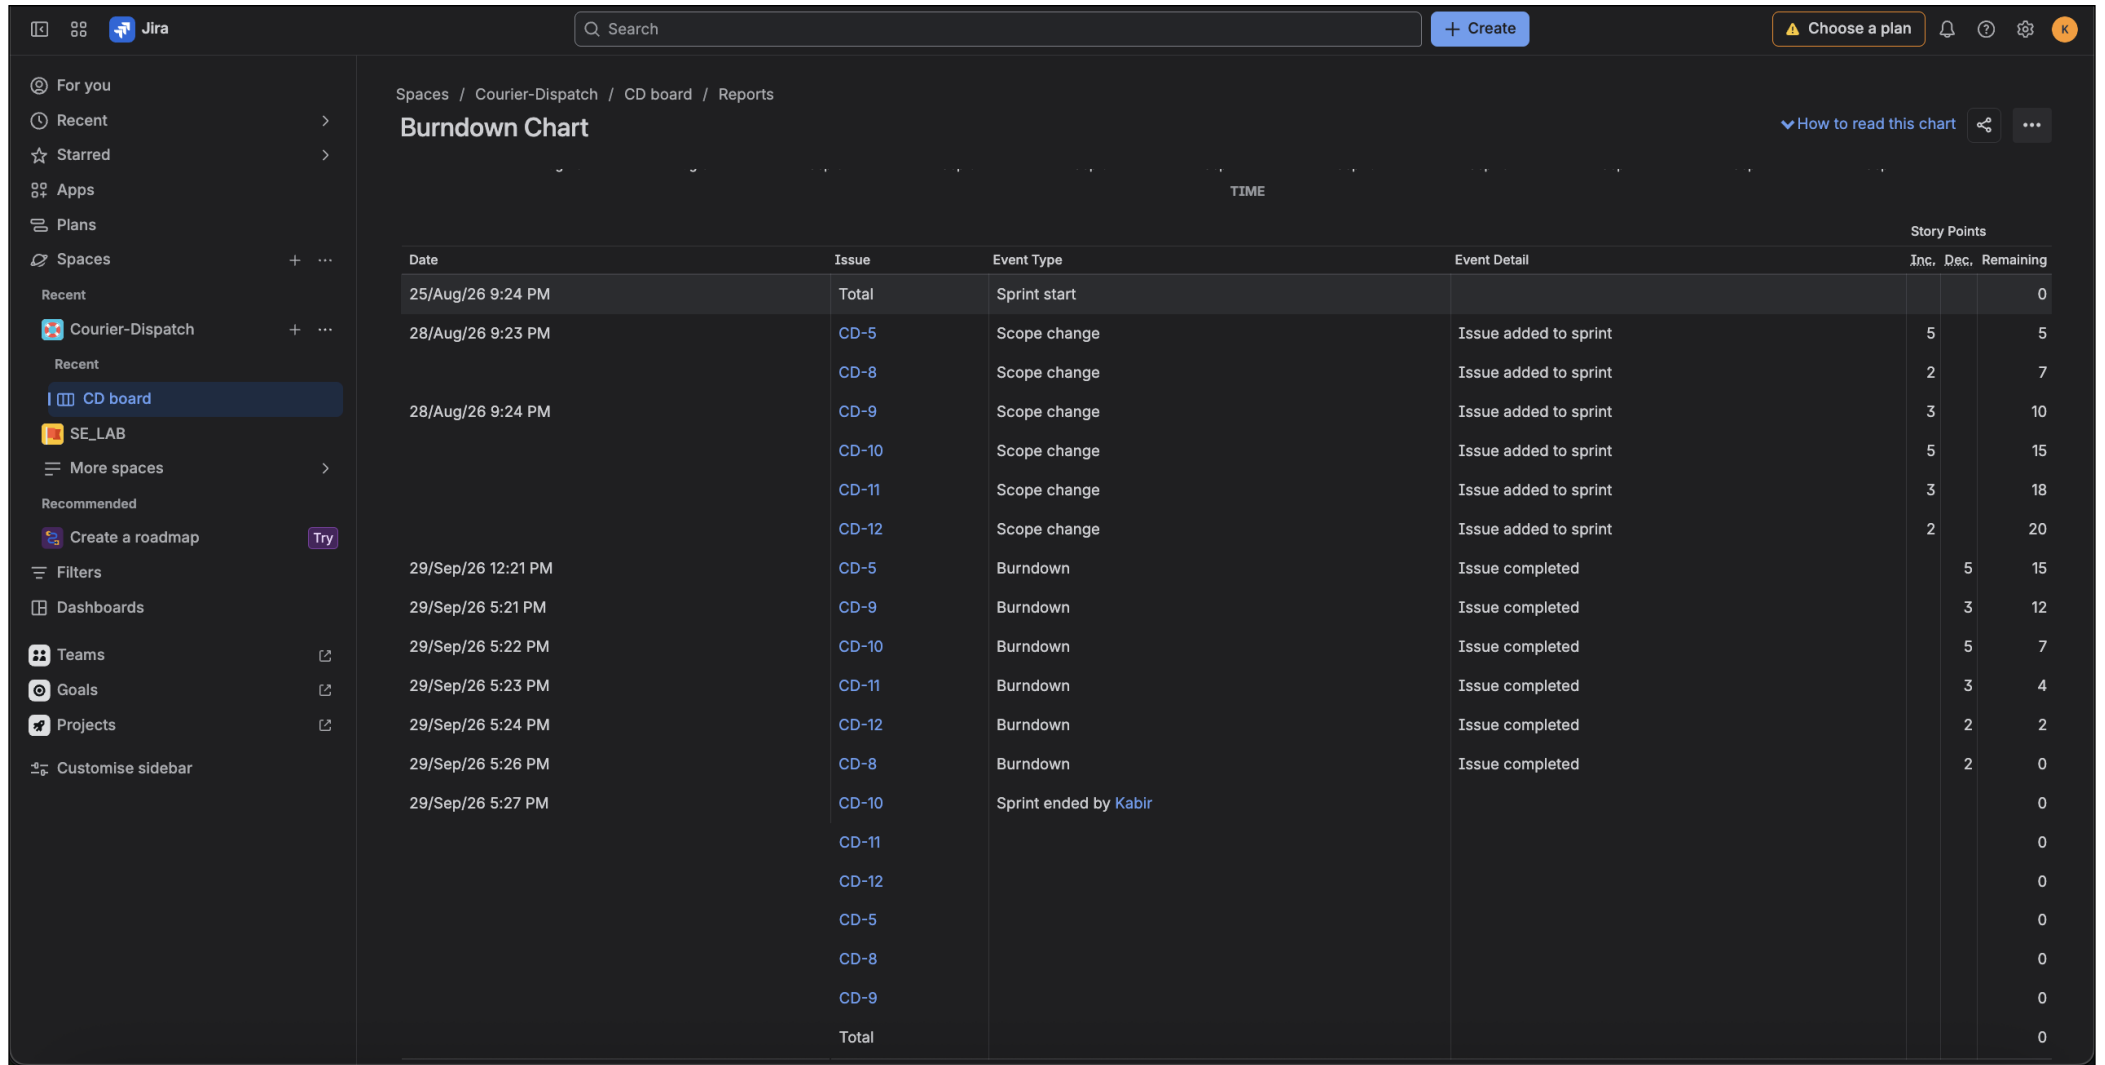


Figure 12. CD Sprint 2 planned with CD-6 and CD-7 (16 points)

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Courier-Dispatch

Recent

CD board

SE_LAB

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Teams

Goals

Projects

Customise sidebar

Spaces / Courier-Dispatch

CD board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search backlog

Version

Epic

Quick filters

Epic

No epic

Courier Request & Dispatch

In-Transit Routing & Tracking

Delivery Completion & Verification

Cancellation Management

Create epic

CD Sprint 2

8 Sep – 22 Sep (2 work items)

1600

Start sprint

CD-6

View Optimized Delivery Route

In-Transit Routing ...

To Do

8

CD-7

Track Rider Location Live

In-Transit Routing ...

To Do

8

Create

2 work items

Estimate: 16

Backlog (0 work items)

000

Create sprint

Your backlog is empty.

Create

Page 12

Figure 13. Sprint 2 board, both stories in To Do

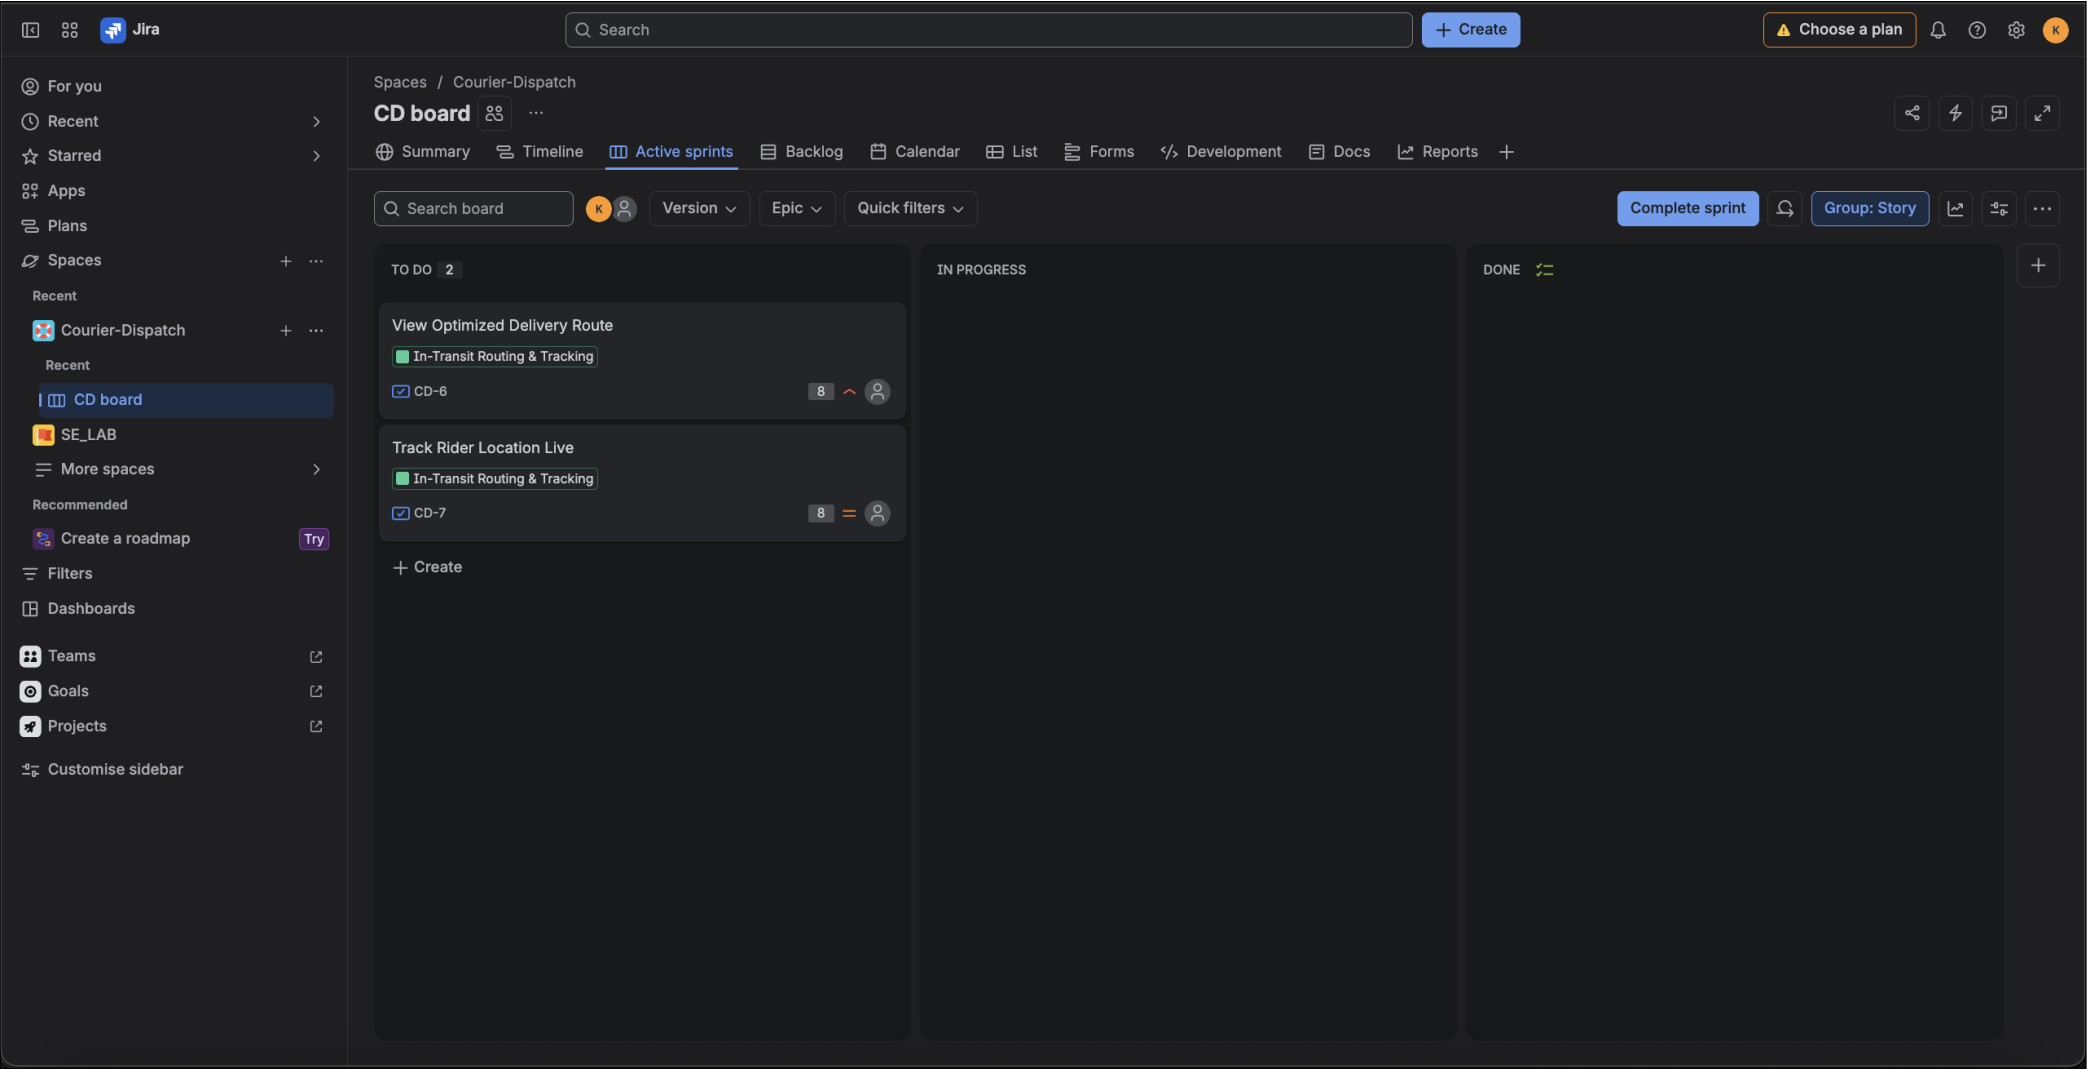


Figure 14. Backlog after Sprint 2 was completed

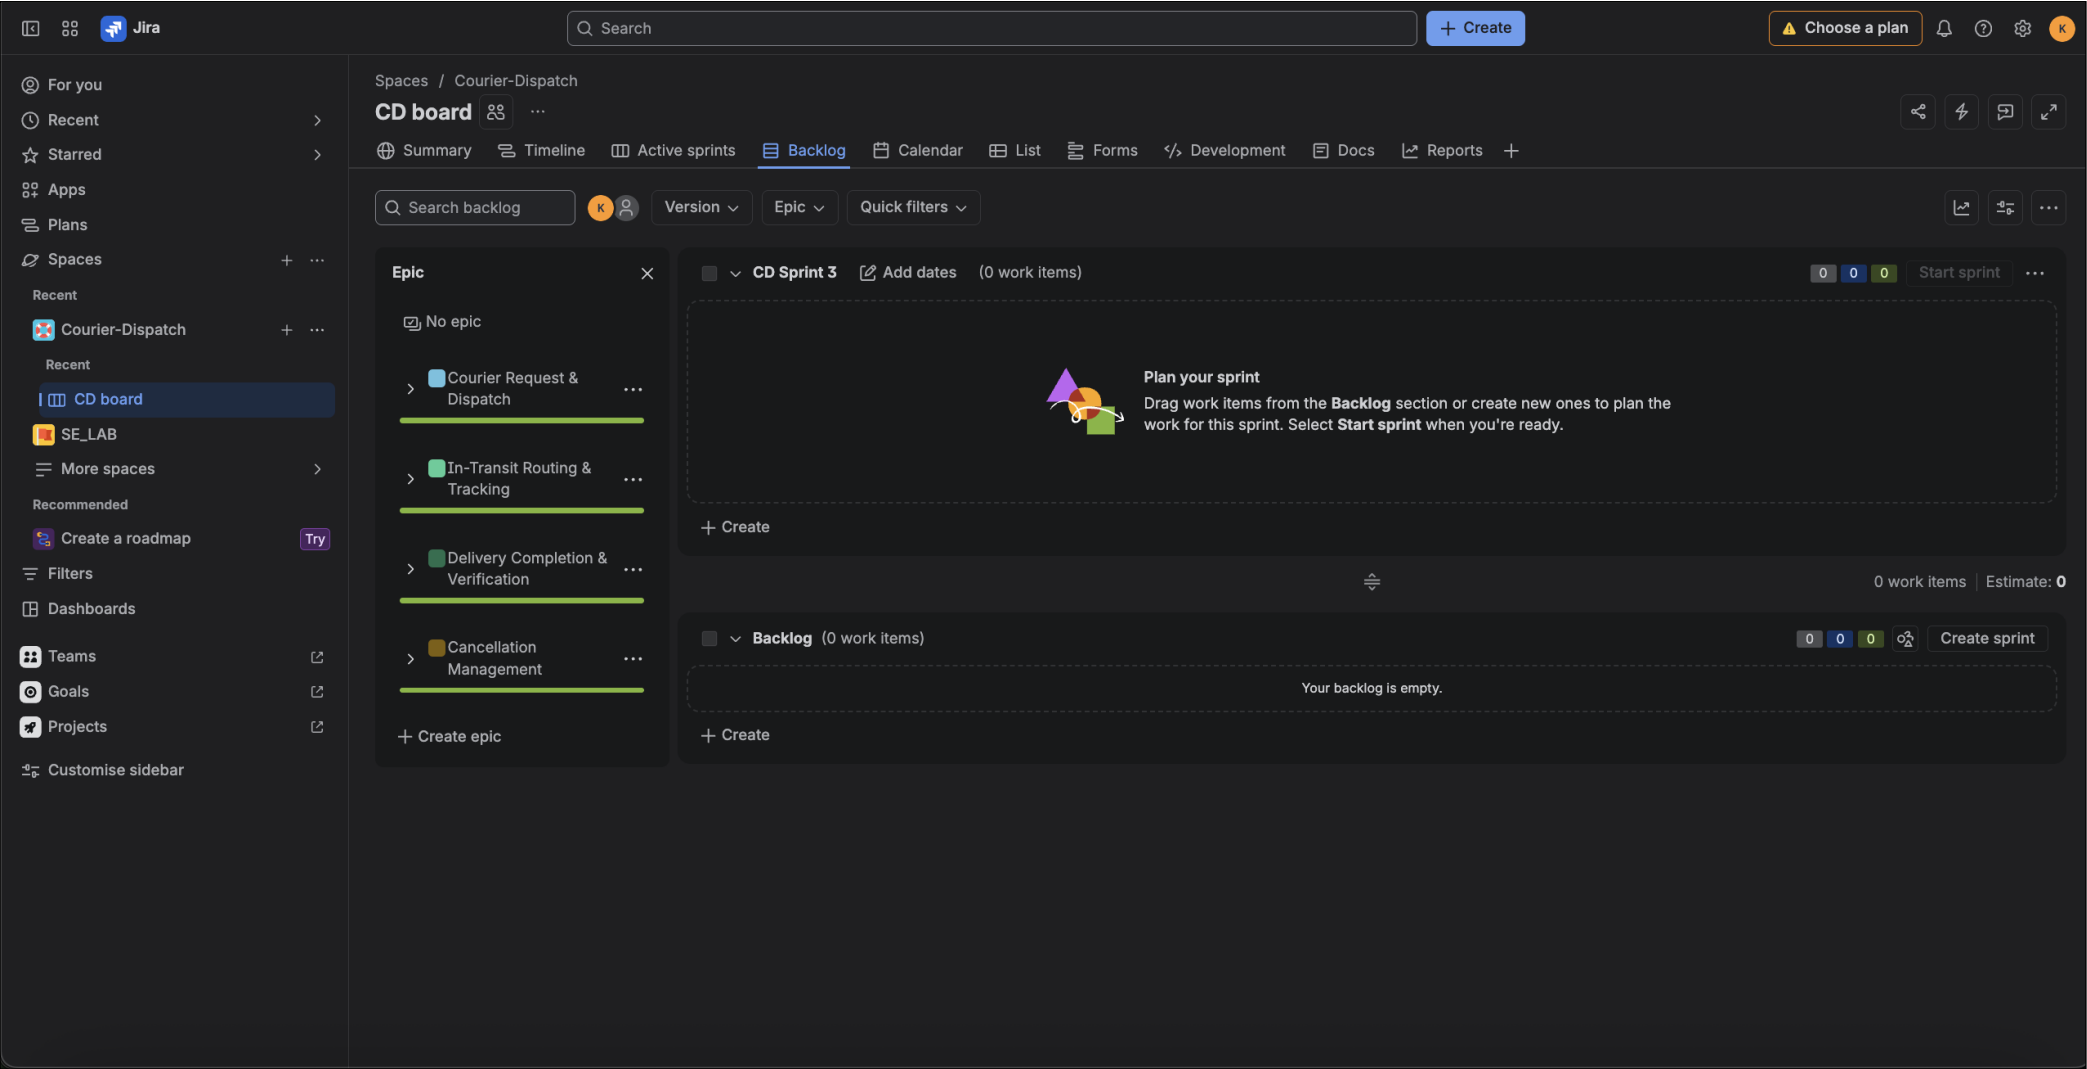


Figure 15. Burndown chart for CD Sprint 2

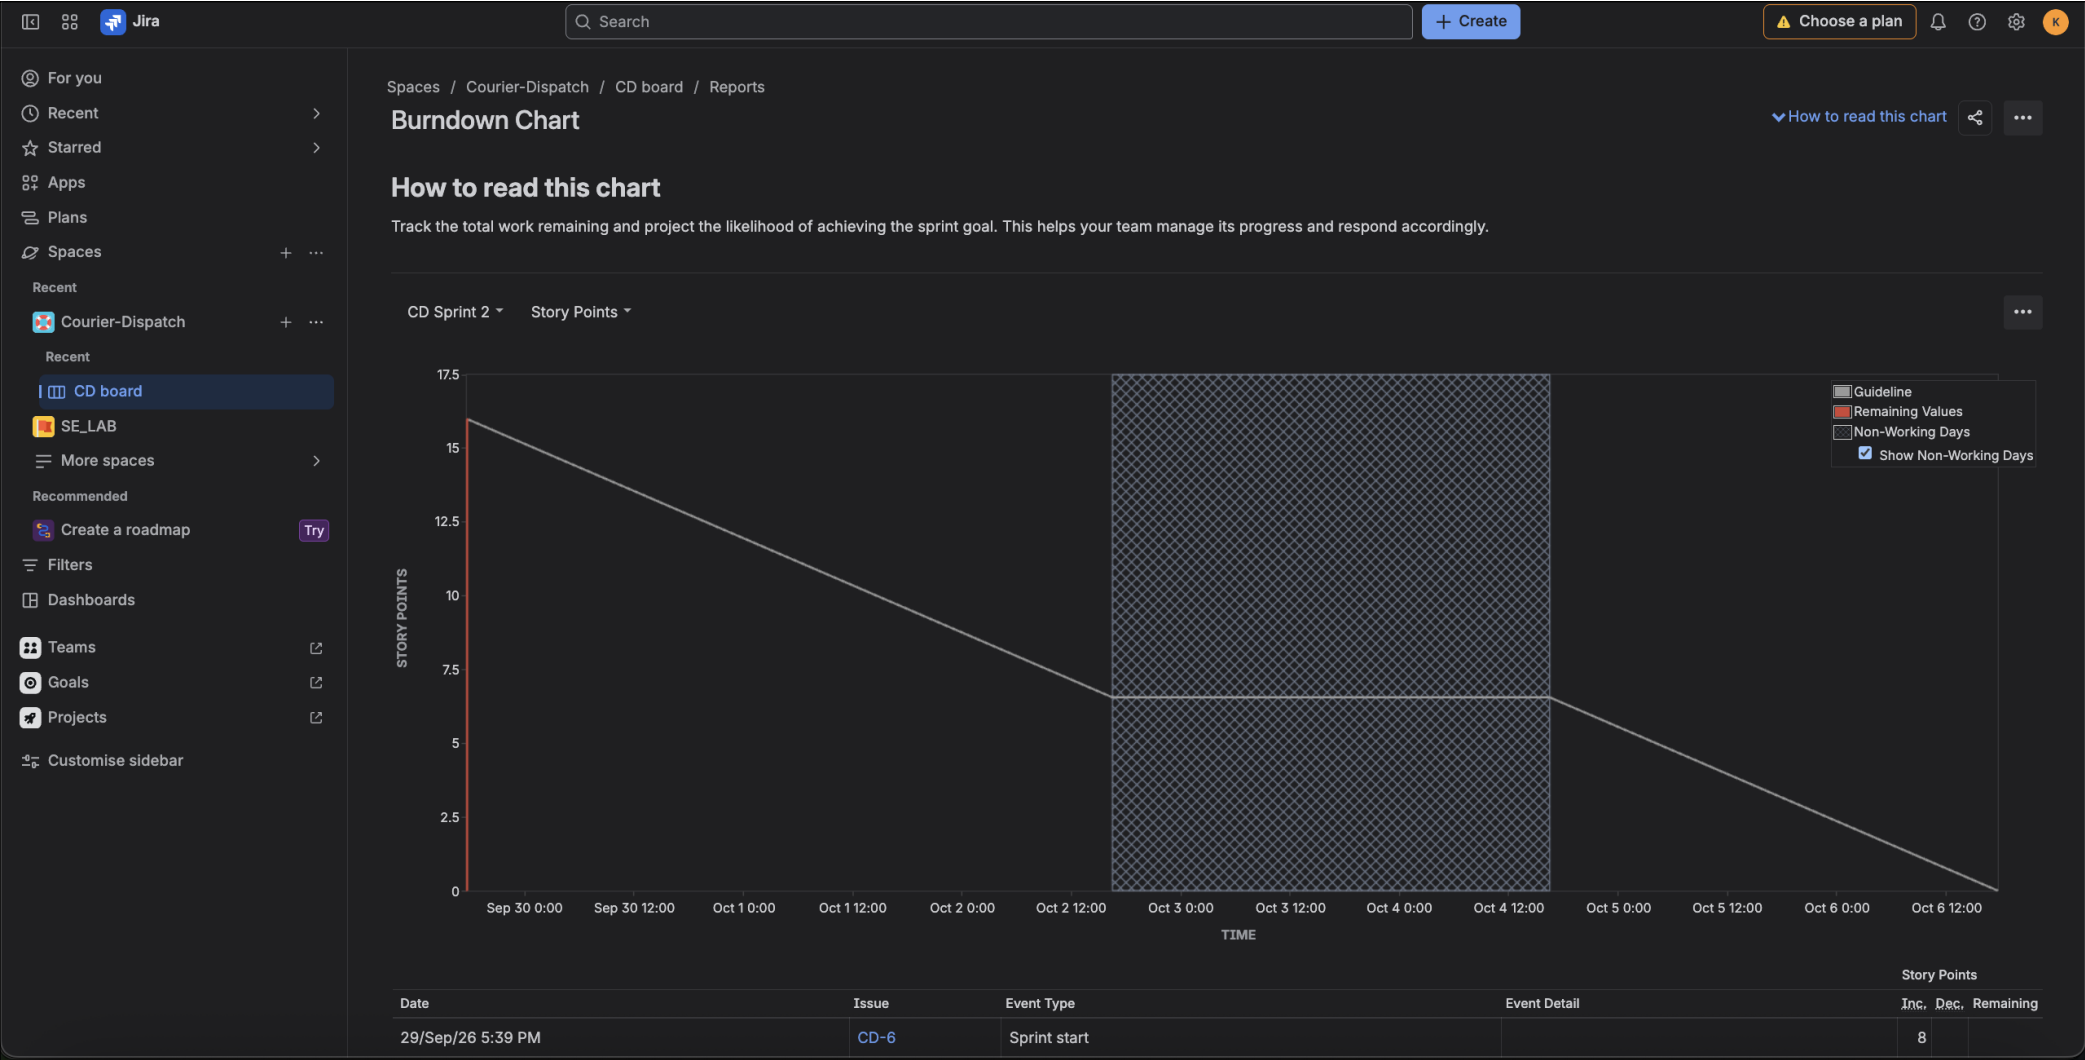


Figure 16. Burndown chart table for CD Sprint 2

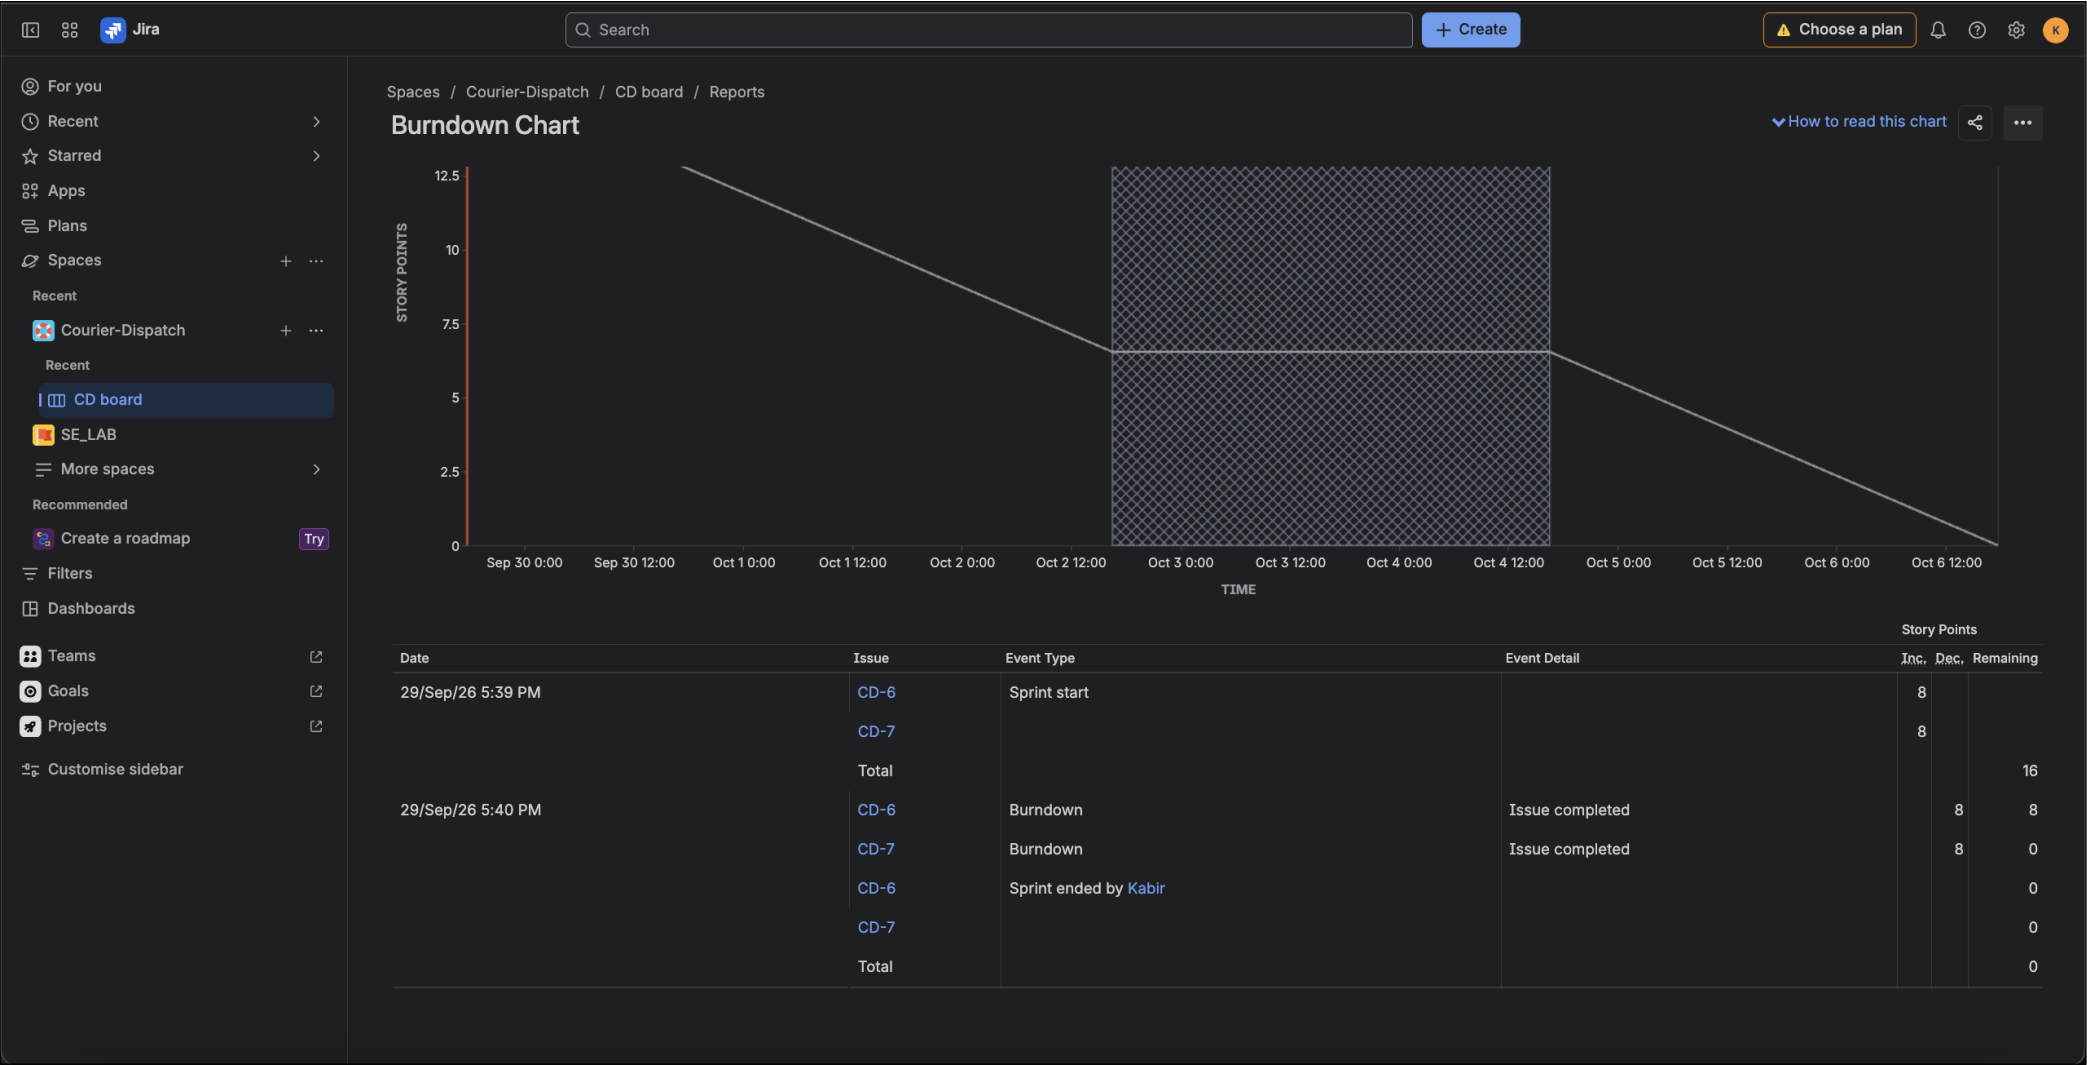


Figure 17. Sprint 3 board with stories in To Do, In Progress and Done


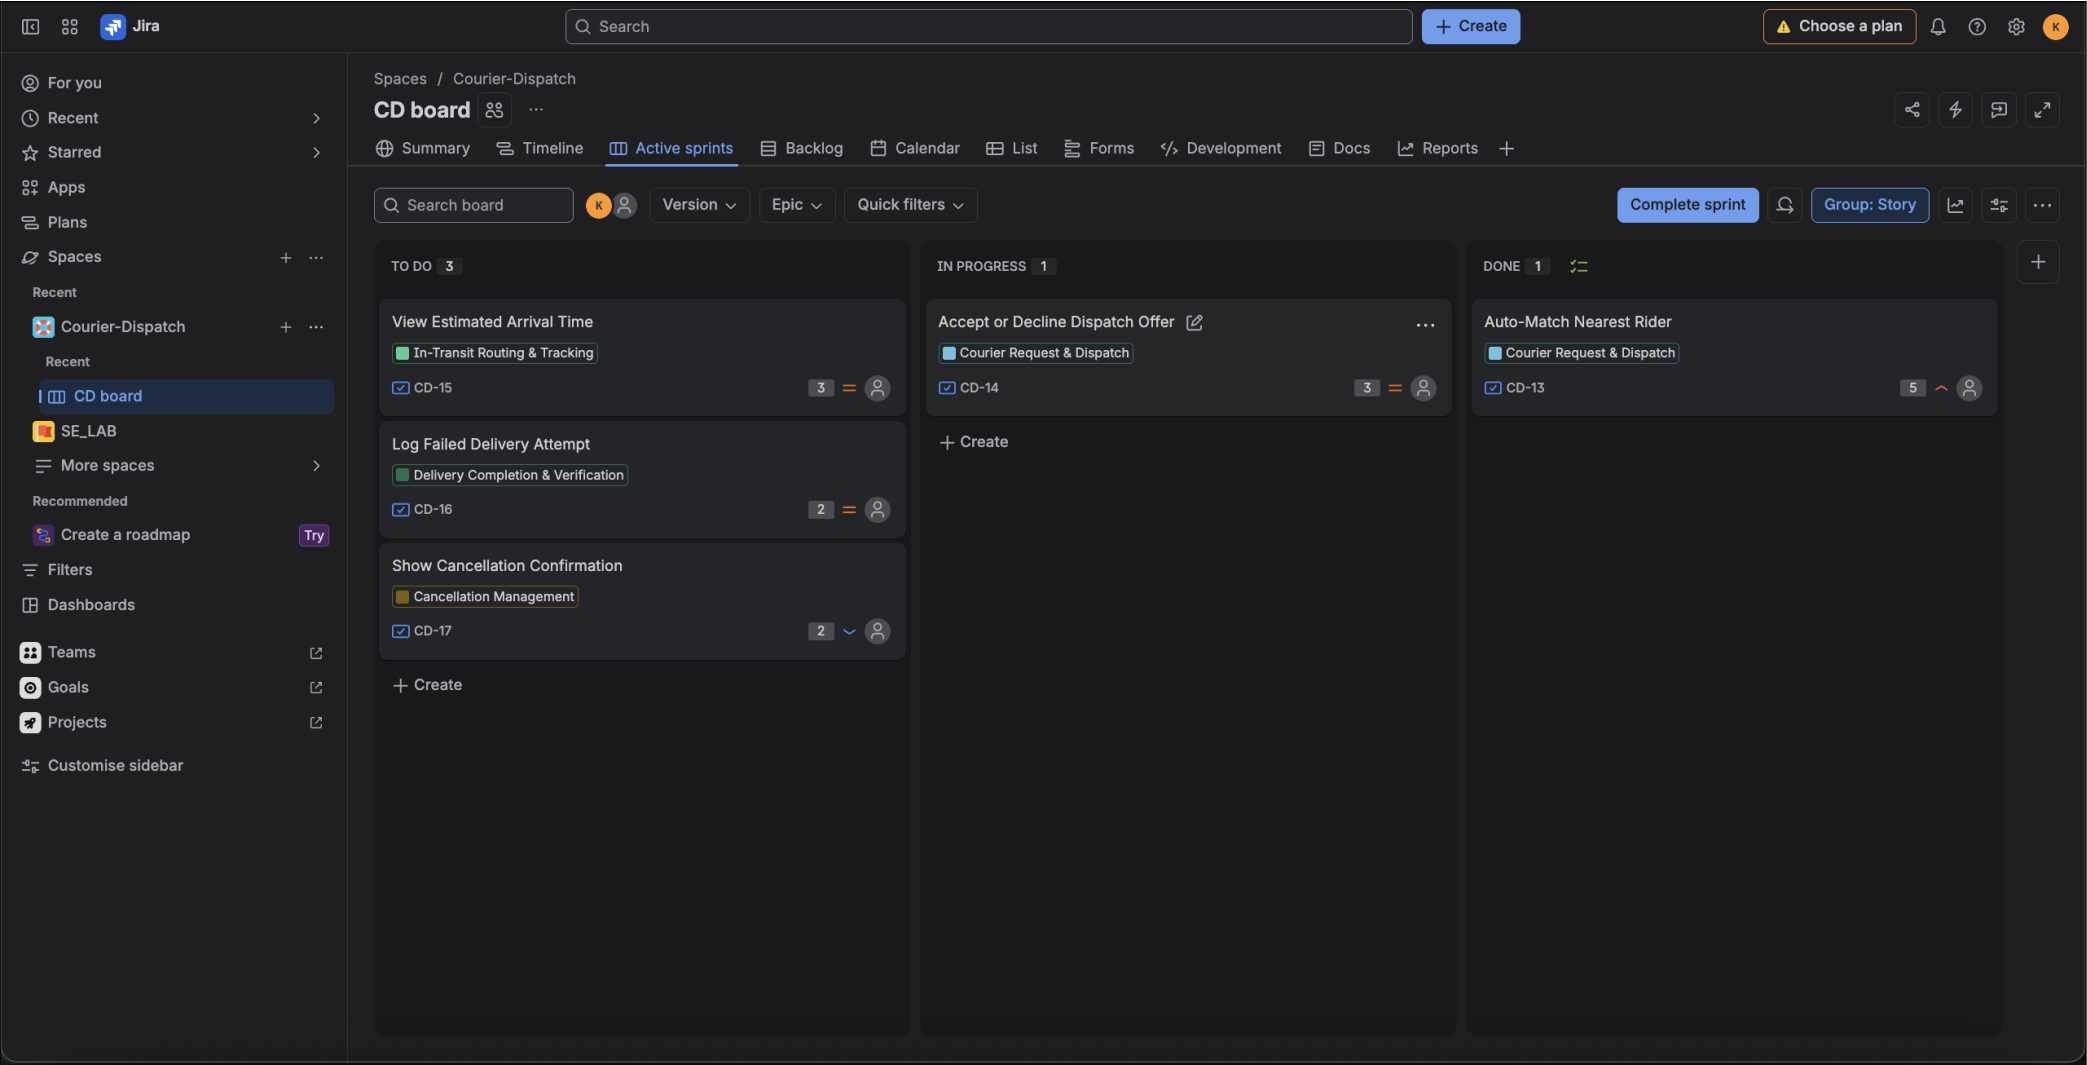


Figure 18. Burndown chart for CD Sprint 3

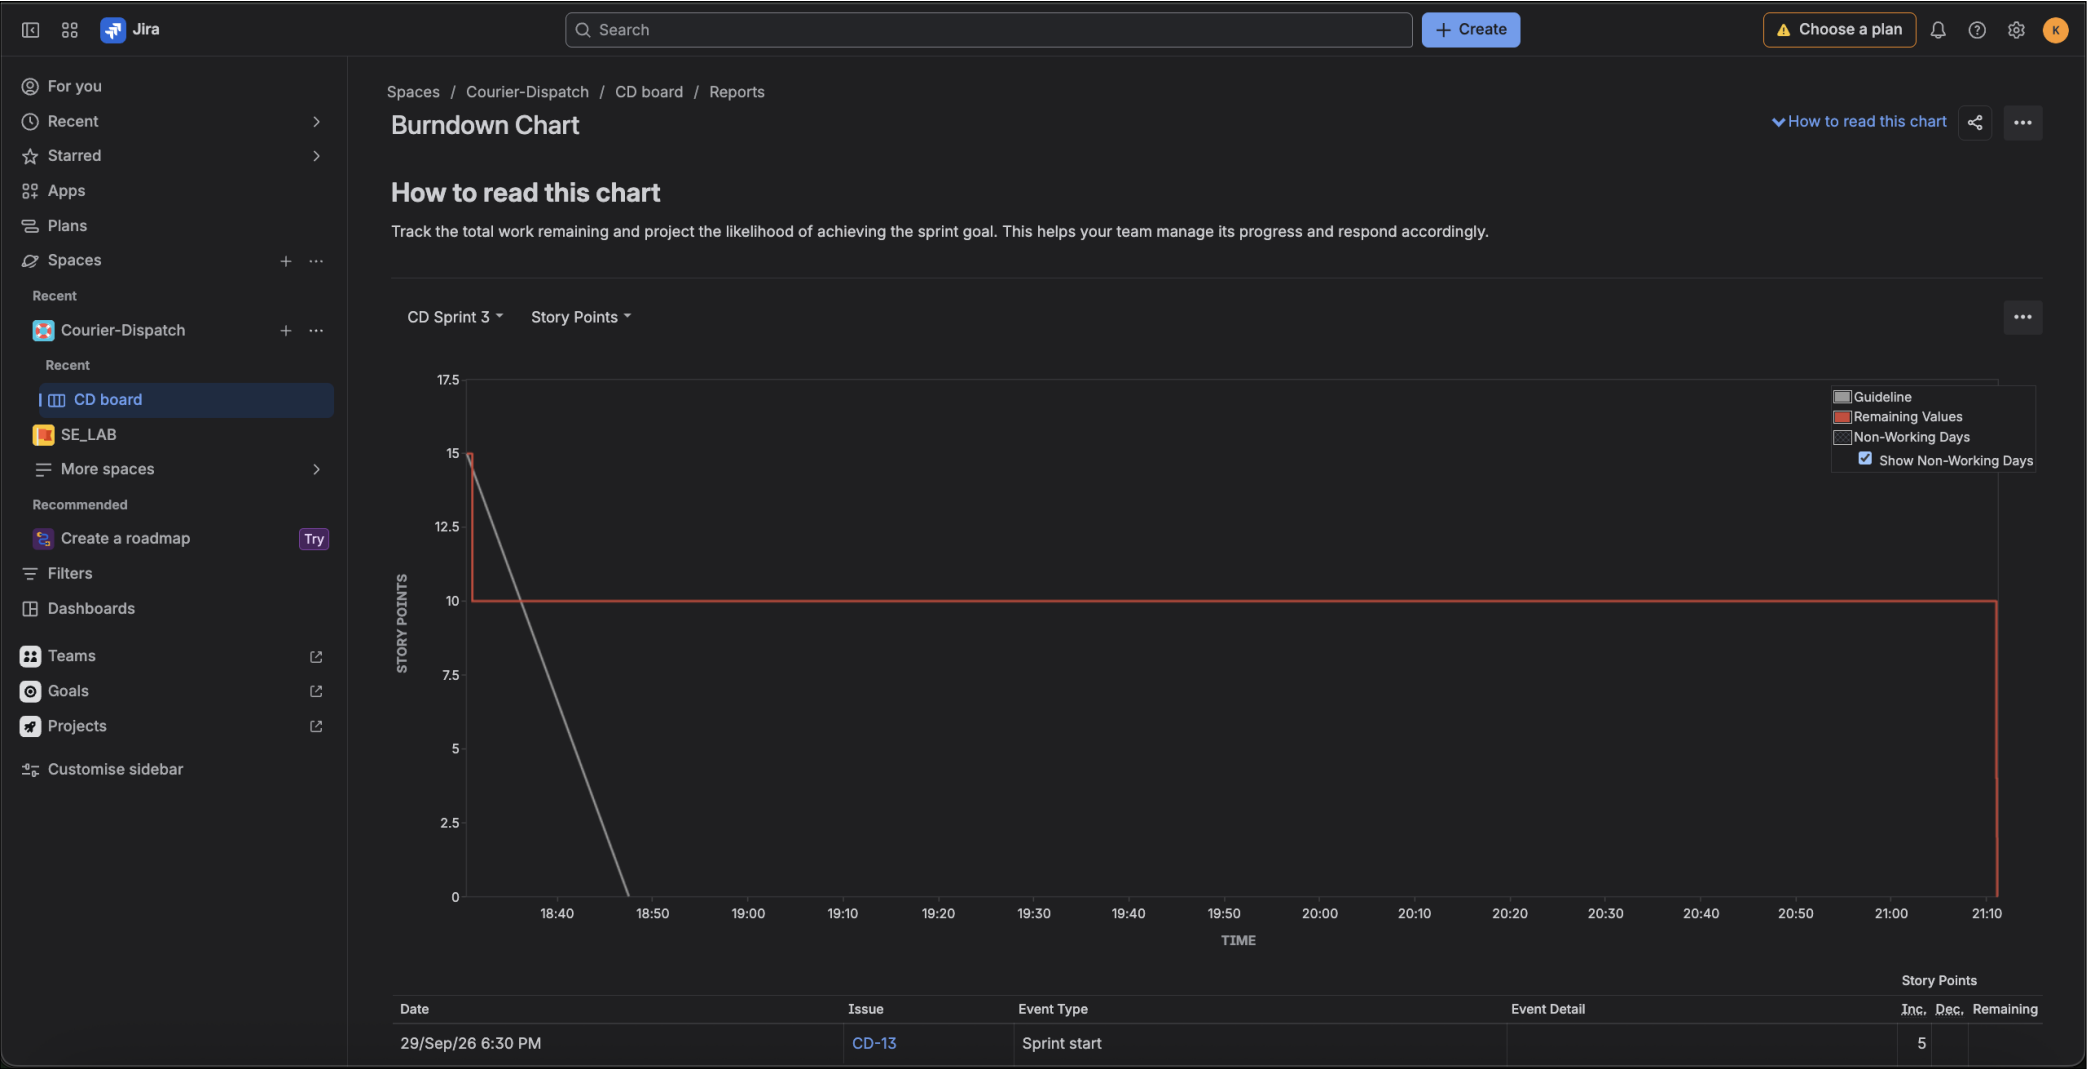

Lab 2: Reflection Questions

Kabir Raju G PES1UG24CS210

1. Did your estimations reflect the actual effort?

I gave the stories 2, 3, 5 and 8 points. The two 8 point stories (CD-6 and CD-7) were the biggest ones, the small ones like updating the delivery status got 2. I think the sizes were fair for planning, but since this is a simulated sprint every story was finished in a few minutes, so I could not really check if 5 points took more effort than 2. One mistake I made was adding the story points after Sprint 1 had already started, so Jira counted them as work added during the sprint. In Sprint 2 and Sprint 3 I set the points before starting.

2. Was your backlog well-prioritized?

Mostly yes. I gave High priority to the main delivery flow: Request a Courier, Mark Parcel as Delivered and Verify Recipient OTP, because the system does not work without them. Update Delivery Status and the cancellation stories were Medium. The 8 point tracking stories were left for Sprint 2 since they are big. Looking back, CD-6 (View Optimized Delivery Route) is High priority but I put it in the later sprint, so I should have split it into smaller stories and started part of it in Sprint 1.

3. How did your simulated sprint align with your plan?

Sprint 1 had 6 stories worth 20 points and all of them were moved to Done, so nothing was left over. Sprint 2 had 2 stories worth 16 points and both were also completed. The difference from a real sprint is that I moved the cards in one sitting instead of over a week. The Sprint 1 dates (25 Aug to 8 Sep) were already in the past when I did the work, and the story points were added late, so the chart did not match the plan. I also ran a Sprint 3 with 5 new stories (15 points) to try for a cleaner chart, but I finished the cards after the sprint window had ended, so that chart is also flat until the end.

4. What insights did the burndown chart give about your team's capacity?

In Sprint 1 the red line is flat at 20 for a long time and then drops at the very end. This is because the stories were added to the sprint after it started and nothing was marked Done until the end, which shows that the chart depends on when the work is actually updated. In Sprint 2 the chart starts correctly at 16 and the guideline goes down as a straight line, but both stories were finished in the first minute, so the red line falls right at the start, far below the guideline. This shows the sprint was too small for the time given. The team finished 20 points in Sprint 1 and 16 in Sprint 2, so about 18 points per sprint looks like a reasonable amount to plan for next time.
